


TorqFall — Venue Scenarios & Build Plan v1

0. The three scenarios at a glance

	A — Indoor AC raw hall	B — Indoor AC sports turf hall	C — Outdoor turf ground
What it is	Empty AC hall / mall unit / banquet floor — nothing exists on site	Futsal/badminton-class turf facility, indoor, AC, walls up	Open-air cricket/football-style ground, no AC
Ground	We lay our own turf for the lane + Tier-3 pen	We still lay our own turf for the lane + pen — RC grip/look is a build spec, not reused from the venue's own surface	We still lay our own turf for the lane + pen
Barrier	Soft noodle-on-sandbag rail, full ~9 m lane length, both sides	Soft noodle rail on the one open side only — the venue's own walls contain the rest	Soft noodle rail, full length — the ground's own boundary backs it up
Hard barricades	None in any scenario — TorqFall has no boarded pitch; every obstacle and every edge is soft, self-righting foam (rulebook §3, §7)	None	None
Driver stand	Rented platform sections (not DIY — needs doc §4)	Rented platform sections	Rented platform sections, under the tent
Weatherproofing	N/A — already indoors	N/A — already indoors	Needed — tent over stand/pit/DJ/seating
Cooling	Already AC	Already AC	Portable AC/cooler, optional
Capex (build-only, ex-venue)	Same gauntlet-kit build as B and C — the kit doesn't change by venue	Same gauntlet-kit build as A and C	Same kit + the one unavoidable extra: tent (+ optional AC)
Control	Full — layout, sightlines, branding on every surface	Partial — lane orientation fixed by the room's shape	Full on the ground, weather is the wildcard
Best for	A branding-heavy shoot if budget allows, since nothing pre-exists to work around	The fastest, cheapest way to get the gauntlet live on camera	A genuinely large, cheap ground with good weather odds for the date

1. Scenario A — Indoor AC raw hall

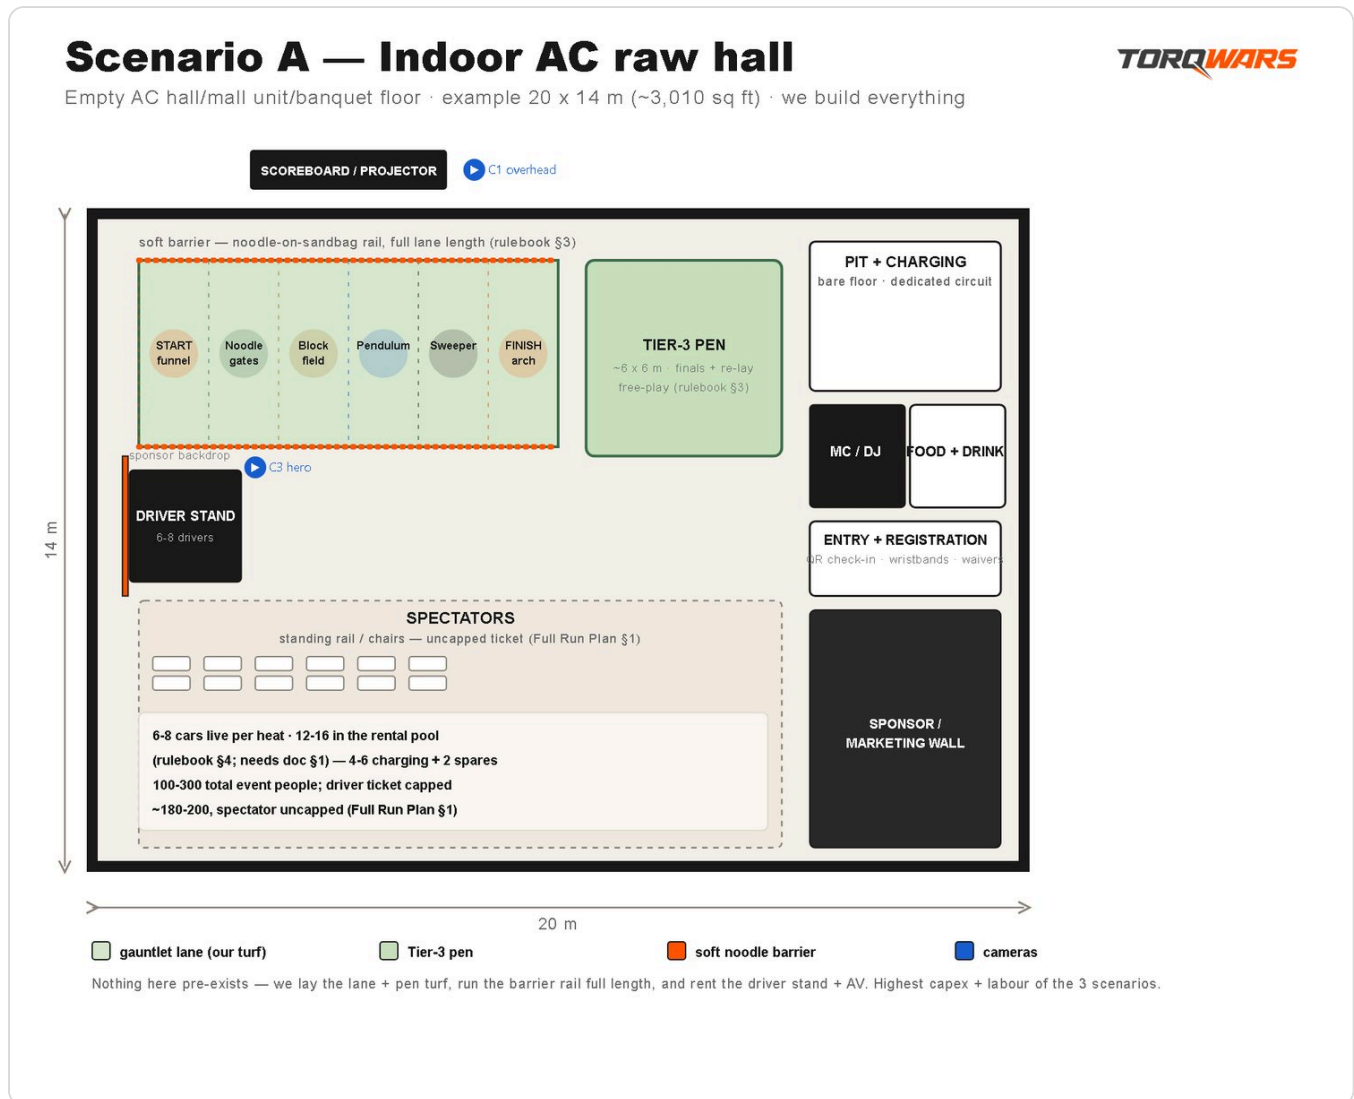

What we'd need:

- The gauntlet lane itself — **~9 x 4 m**, per [2 - TorqFall \(rulebook\)](#) §3, laid in our own artificial turf
- The **~6 x 6 m Tier-3 pen laid alongside the lane at morning setup** (rulebook §3) — for Hex-a-Fall, The Grinder, King of the Hill, and it doubles as the free-play space during round-swaps
- Soft side barriers the full lane length, both sides — noodle-on-sandbag rail (rulebook §3), the ONLY containment TorqFall uses; no boarded pitch, no hard barricade
- Start and finish arches with LED, one each end of the lane
- A rented driver stand, side-on to the lane, sized to the **6–8 concurrent drivers per heat** (rulebook §2/§3; needs doc §4) — not a DIY build
- An MC/DJ position
- A pit + charging table on bare floor with its own dedicated circuit
- Food/drink stalls
- Entry/registration desk
- A marketing/sponsor wall
- A scoreboard or projector, visible from the lane and the stand

- An overhead camera rig locked on the lane, plus a low finish-line camera


Why it costs more: the room starts empty, so the lane's own turf, the full-length barrier rail, and every show-layer item (stand, AV, branding) are either a build or a rental with nothing to offset the cost against.

Where it wins: total control. Lane orientation, stand position, DJ booth and branding all get placed for the best camera angles, since nothing pre-exists to route around.

What to look for in this venue type

- Clear sq ft with furniture out — needs to comfortably hold the lane + pen (~800–1,200 sq ft of turf per [TorqFall — What The Event Needs](#) §2) plus stand, pit, spectators and stalls inside a ~3,000 sq ft envelope
- Floor: flat, and tolerant of turf tape and sandbag feet for a full day
- AC confirmed for the specific hall being used, not just the building
- Power: enough sockets near the pit and AV positions for a dedicated charging circuit, or confirm genset access (Event Ops Standards §2)
- Noise tolerance for the DJ/MC PA and RC motors for a full afternoon
- F&B rule — in-house only vs outside catering/food-truck allowed vs an F&B minimum
- Load-in: a door wide enough for a turf roll + kit crates, and enough lead time for the ≤4-hour build target (Event Ops Standards §2)

2. Scenario B — Indoor AC sports turf hall

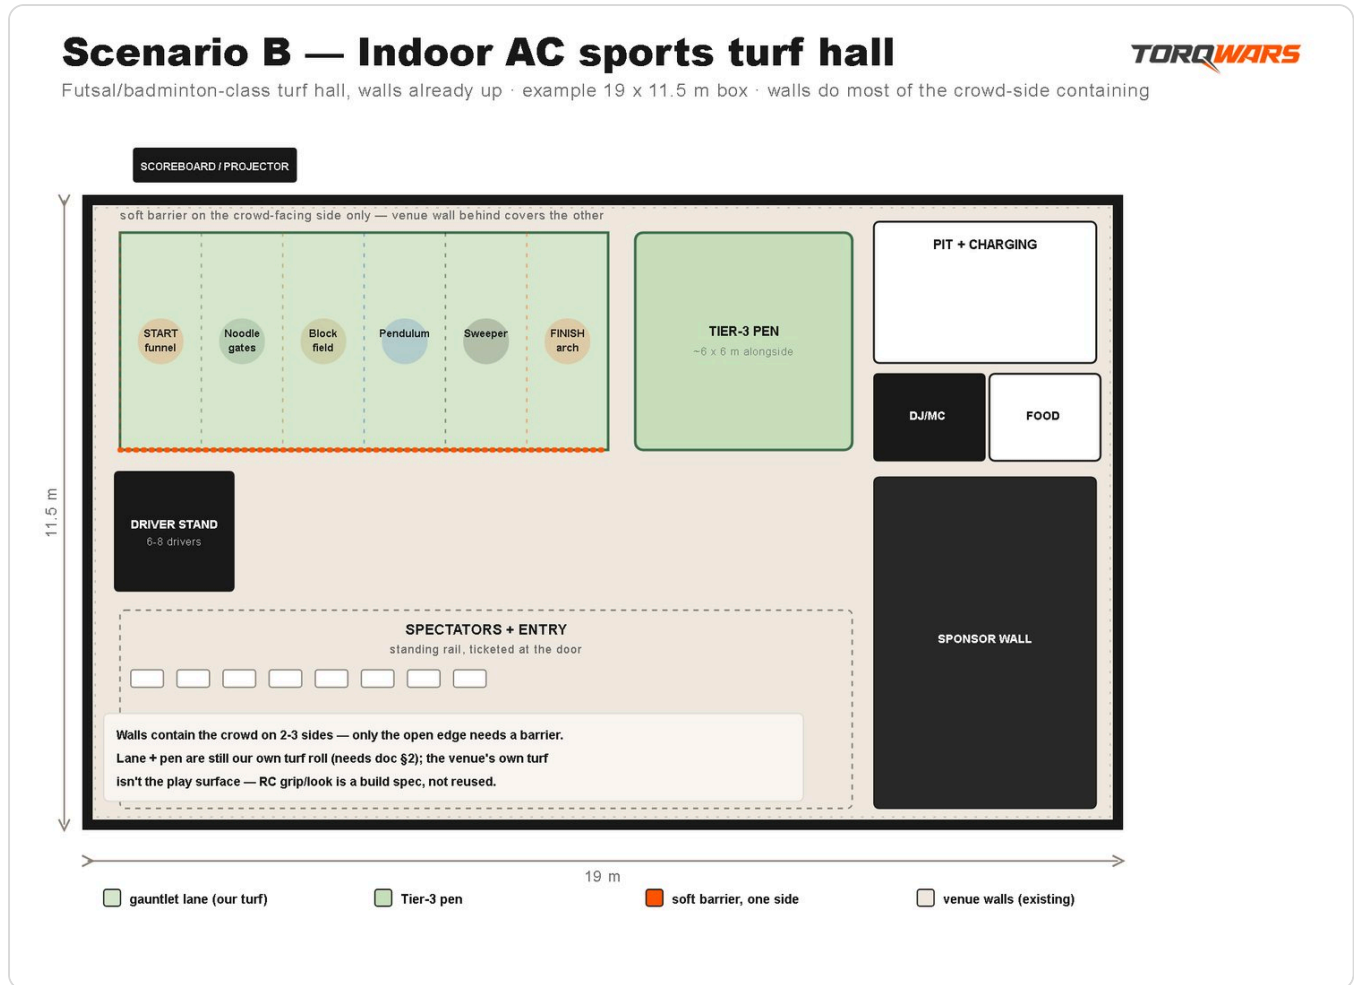

What we'd need: almost nothing structural — the walls and AC are already there; we still bring the lane's own playing surface.

- The gauntlet lane — **~9 × 4 m** (rulebook §3), our own turf roll laid inside the hall
- The **~6 × 6 m Tier-3 pen alongside the lane** (rulebook §3), same turf
- A soft noodle barrier on the **one open side only** — the venue's walls contain the rest
- A rented driver stand, sized to 6–8 concurrent drivers (needs doc §4)
- Pit + charging table
- Watcher standing rail
- A scoreboard or projection
- Entry desk, tucked beside the open door


This is the cheapest scenario to run: no full-perimeter barrier build, no weatherproofing, and the room's own AC and walls do most of the containment work for free.

What to look for in this venue type

- Clear sq ft for the lane + pen (~800–1,200 sq ft, needs doc §2) with the walls actually forming a usable containment line, not just floor space
- Floor: a synthetic sports surface with grip suited to small RC tyres is a bonus, but our own turf roll is still the play surface (RC grip/look is a build spec, not something to gamble on the venue's surface)

- AC genuinely chilled for the hall being booked, not just described as "indoor"
- Power for the pit's dedicated circuit and the AV/scoreboard
- Noise tolerance for DJ/MC + RC motors, especially if the facility runs other courts concurrently
- F&B — whether outside catering or a food truck can dock near the hall
- Load-in: whether the court/turf area can be reached without crossing another booking, and how much of the ≤ 4 -hour build window the facility actually grants

3. Scenario C — Outdoor turf ground

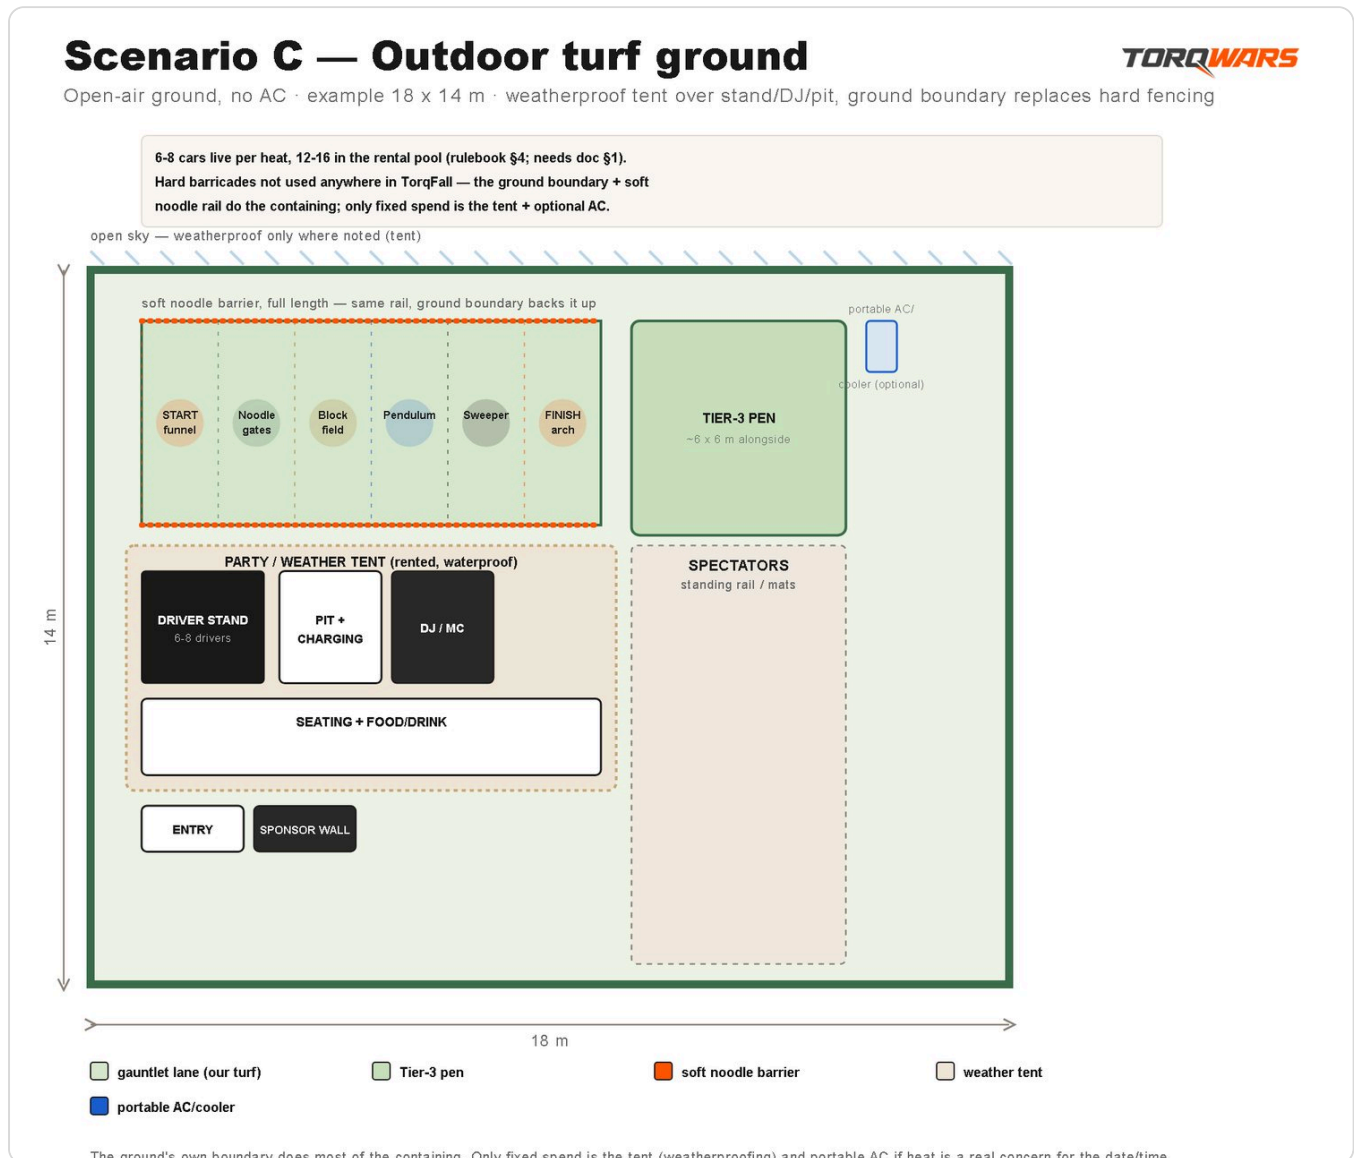

What we'd need: the ground's own boundary does most of the containing; the one real addition is weatherproofing.

- The gauntlet lane — **~9 x 4 m** (rulebook §3), our own turf roll
- The **~6 x 6 m Tier-3 pen alongside the lane** (rulebook §3)
- Soft noodle barrier, full lane length, backed by the ground's own boundary — same rail as the other two scenarios, nothing extra

- A rented **weatherproof party/event tent** over the driver stand, pit, DJ/MC and seating — the one genuinely fixed weatherproofing spend
- A rented driver stand under the tent, sized to 6–8 concurrent drivers (needs doc §4)
- Spectator standing rail/mats beside the tent
- Portable AC/cooler units — optional, priced separately, only if heat is a real concern for the date and time chosen

What to look for in this venue type

- Clear sq ft for the lane + pen + tent footprint, with room left over for spectators without crowding the barrier line
- Ground: level enough that the turf lies flat and sandbag stakes hold; drainage if rain is a real risk for the date
- No AC by definition — confirm shade/time-of-day plan instead, and budget the portable cooler line if needed
- Power: venue mains **plus a generator/battery fallback** (Event Ops Standards §2) — outdoor grounds are the scenario most likely to have unreliable or absent mains
- Noise/DJ terms — outdoor grounds often carry separate community or civic noise rules; confirm on the same call as the sq ft question
- F&B — whether a food truck can park and serve directly on-site
- Load-in: vehicle access to drop a turf roll, tent, and kit crates directly at the pitch edge

4. DIY vs vendor — keep it capex-light


The instruction driving this plan: **reduce vendor dependence wherever we can build it ourselves.** TorqFall's DIY split is simpler than a boarded-pitch game's — there's no hard barricade to build at all, and the driver stand is a rental in every scenario, not a build.

Item	Build it ourselves (DIY)	Use a vendor	Why
Gauntlet obstacle kit — arches, pendulum, sweepers, spinner gate, ramp, whack tunnel, Collapse-Gate wall	Yes — one modular kit builds all ~21 rounds (rulebook §4; TorqFall — Level Directory v1), ≈₹40,000–61,000 one-time + per-event consumables (TorqFall — What The Event Needs §3)	Spinner gearmotors/PWM modules bought in, then assembled by us	Same kit reused every event regardless of venue; only the layout inside the lane changes per round
Soft barrier rail + bump rings + queue posts	Yes — noodle-on-sandbag joinery, needs doc §3/§8	—	Cheap, reusable, and the only containment TorqFall needs in any scenario
Turf (lane + Tier-3 pen)	—	Vendor — turf dealer, ~800–1,200 sq ft (needs doc §2)	Bulk artificial grass is a dealer buy, not a build; the same roll travels to every scenario

Item	Build it ourselves (DIY)	Use a vendor	Why
Driver stand	—	Vendor — rented certified staging (needs doc §4)	"People stand on it → rent certified staging, don't DIY this one piece"
Pit + charging table	Mostly buy , minimal DIY setup	Table, chargers (or club-supplied), LiPo bags, extinguisher	Mostly a shopping list, per Event Ops Standards (all games) §5 and Car Fleet, Scale & Protection §5
Cars + pit crew	—	Vendor — rented RC club fleet, 12–16 cars (rulebook §4; needs doc §1)	No owned fleet for event #1; the club brings batteries, spares and 2 pit crew
Branding print (backdrop, banners)	—	Vendor — flex/fabric print (needs doc §5)	Print quality matters on camera; DIY printing looks DIY
Weatherproof tent + portable AC (Scenario C only)	—	Vendor — rented per event	Not buildable; renting is the only realistic route
DJ + sound, MC	—	Vendor or a friend with gear	Standard party-hire items, not worth building
Food/drink	—	Vendor — food truck or light catering	Never DIY catering for a public event
Scoreboard / AV	Laptop + bracket if already owned	Projector/screen/PA rental (needs doc §5)	Cheapest workable AV is fine for event #1

Net effect: across all three scenarios the only physically built items are the gauntlet kit and the barrier rail — both fully reusable at every future event. Turf, driver stand, branding print, DJ/sound, food, and (Scenario C only) the tent and AC are the recurring vendor lines.

5. Build timeline — location in 5 days, build in 7

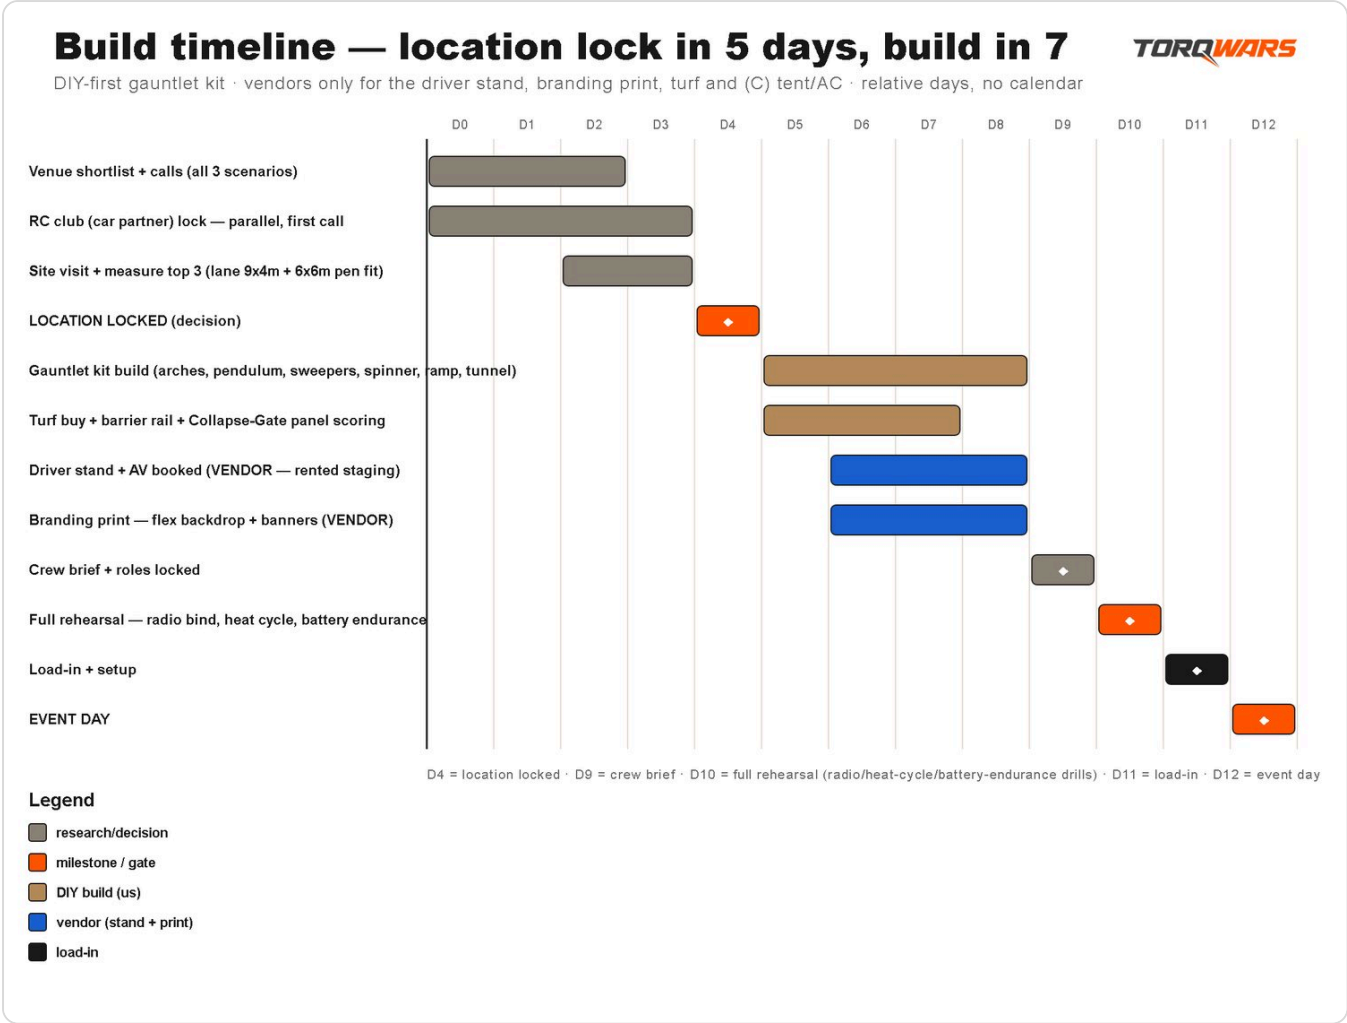

Day	Milestone
D0–D3	Venue shortlist + calls across all 3 scenarios; in parallel, the RC club (car partner) call goes out on D0 — "nothing runs without it" (TorqFall — Full Run Plan §1)
D2–D3	Site visit + measure the top 3 candidates — confirm the ~9 × 4 m lane and ~6 × 6 m pen actually fit (rulebook §3)
D4	LOCATION LOCKED — the decision that gates every build choice after it
D5–D8	Gauntlet kit build — arches, pendulum, sweeper bars, spinner–gate bench test, ramp, whack tunnel (TorqFall — What The Event Needs §3 ; TorqFall — Full Run Plan DIY build weekend)
D5–D7	Turf buy, barrier–rail assembly, Collapse–Gate panel scoring — in parallel
D6–D8	Driver stand + AV booked (vendor — rented staging, needs doc §4)
D6–D8	Branding print ordered (vendor , the one item with real lead time)
D9	Crew brief + roles locked (12 on the day — needs doc §7; TorqFall — Full Run Plan §6)

Day	Milestone
D10	Full rehearsal — max-pack radio bind test, heat-cycle timing, reset drills, Collapse-Gate wall test, battery-endurance drill (TorqFall — Full Run Plan §1)
D11	Load-in + setup — chalk the lane, roll turf, barrier rail, arches, driver stand, pit, AV (TorqFall — Full Run Plan §2)
D12	EVENT DAY

Why location comes first: the lane's orientation, the barrier run, and whether a tent is needed all depend on which scenario wins. Nothing in §4's build list should be bought before D4.

Compressing the timeline: if a venue confirms before D4, everything after it can shift left by the same number of days — the gauntlet kit build is a fixed ~4-day job regardless of scenario, but the driver-stand and branding-print bookings (vendor lead times) are the items least compressible.
