

TorqBall — Venue Scenarios & Build Plan v1

Three venue types for the TorqBall short-run event, compared side by side, with a floor plan for each and one build timeline. Desk research, Mumbai, Sept 2026 — nothing below has been phone-confirmed or booked. Game rules stay as in [TorqBall — Rulebook](#); the fleet rule stays as in [Car Fleet, Scale & Protection](#). Starts from today, **2026-09-14**: location locked by **2026-09-18** (5 days), build complete by **2026-09-25** (7 days), event window opens **2026-09-26**.

0. The three scenarios at a glance

	A — Indoor AC raw hall	B — Indoor AC sports turf	C — Outdoor turf
What it is	Empty AC hall / mall unit / banquet floor — nothing exists on site	Badminton/cricket/football turf, indoor, AC	Open-air cricket/football ground, no AC
Ground	We lay our own turf/gym mat	Already down	Already down
Barricades	Full build, all 4 sides — no walls to use	Mostly skipped — walls/net contain 3 sides, one soft line	Mostly skipped — ground boundary + rented inflatable air-wall
Goals	Build or buy (Decathlon) + LED, from scratch	Build or buy + LED	Build or buy + LED
Ramps	Same modular kit in all 3	Same modular kit in all 3	Same modular kit, under a shade sail
Weatherproofing	N/A — already indoors	N/A — already indoors	Needed — tent over stand/DJ/seating
Cooling	Already AC	Already AC	Portable AC/cooler units, optional
Capex (build-only, ex-venue)	Highest — everything fabricated	Lowest — reuses venue structure	Middle — tent + inflatables replace hard barricades
Control	Full — layout, branding, sightlines on every surface	Partial — pitch orientation fixed by the turf shape	Full on the ground, weather is the wildcard
Best for	A hero, branding-heavy shoot if budget allows	The fastest, cheapest way to get a live match on camera	If a genuinely large, cheap ground is available and the date has good weather odds


1. Scenario A — Indoor AC raw hall

Scenario A — Indoor AC raw hall

TORQWARS

Full-build rig · example 20 x 15 m (~3,230 sq ft) empty AC hall/mall unit/banquet floor · we build everything

SCOREBOARD / SCREEN  C1 overhead

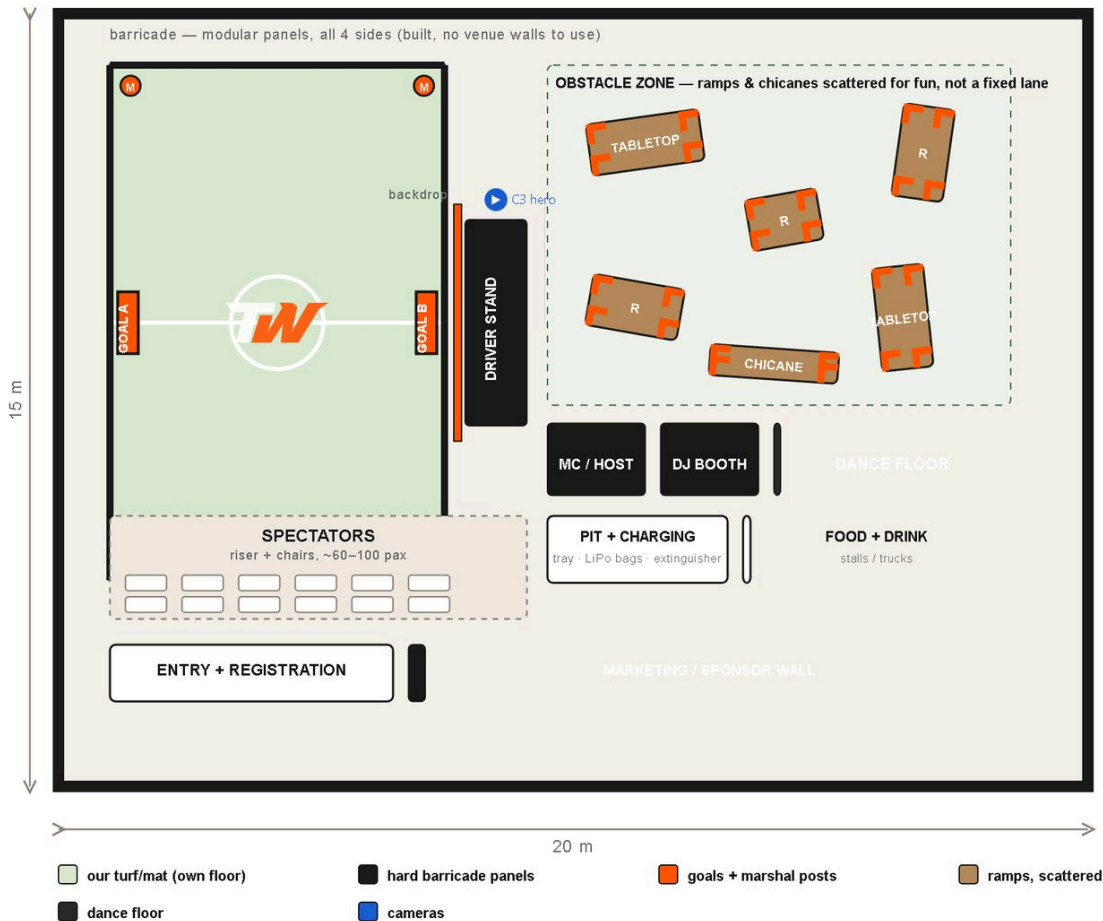

Everything here is built by us — highest capex + labour of the 3 scenarios, but full control of layout, sightlines and branding on every surface.

What we'd need to build, top to bottom:

- Modular barricade panels on all four sides — nothing here is contained by the venue itself
- Our own turf or gym-mat flooring for the pitch — **6.5 x 10 m ≈ 700 sq ft**, the real dimension from [TorqBall — Rulebook §3](#), not a guess
- Two goals with LED, built or Decathlon-bought
- The ramp kit **scattered across an open "obstacle zone"** beside the pitch, not a single padded lane — chicanes and jumps placed informally so cars find them while free-driving, the way the field itself makes the game fun
- A driver stand facing the pitch, backdrop behind it for the hero shot — **seats sized to the Big Party peak (8-12 concurrent drivers), not to total attendance**, per Rulebook §4/§5
- An MC stand
- A DJ booth

- A dance floor big enough for 20–30 people
- Spectator seating (riser + chairs, ~60–100 pax)
- Pit + charging table
- Food/drink stalls
- Entry/registration desk
- A marketing/sponsor wall
- A scoreboard or screen
- An overhead camera rig

Why it costs more: every one of those is a fabrication or a rental, because the room starts empty. This is the only scenario where hard barricades run the full perimeter — budget them like the boarded-arena spend in [TorqBall — What The Event Needs](#) §2, not the light noodle-line from a turf scenario.

Where it wins: total control. The pitch, stand, DJ booth and dance floor can all be positioned for the best camera angles and the branding covers every surface, since nothing pre-exists to work around.

Venue shortlist (web desk research — not phone-confirmed)

Venue	Area	Type	Size	AC?	Rate	F&B	Crowd-pull	Tier
Mehboob Studios	Bandra W	Film studio → concert venue	Large soundstage, sq ft not listed	Unconfirmed (studio — may need portable AC)	Not listed	Likely outside catering allowed	A — active concert venue	A
Hard Rock Cafe	Andheri W	Restaurant/music venue	Banquet 375–600 pax	Yes	Not listed	In-house kitchen+bar, likely F&B min	A — global nightlife brand	A
Doolally Taproom	Andheri W	Brewery/taproom	~250-guest hall claim	Yes	Not listed	In-house brewery	A — existing games+beer crowd	A
Todi Mill Social (Kamala Mills)	Lower Parel	Lounge/bar	300 seated / 450 floating	Yes	Not listed	In-house bar/kitchen	A — densest bar-hop district in Mumbai	A
NESCO / Bombay Exhibition Centre	Goregaon E	Exhibition halls	Smallest hall ~22,700 sqft — ask for a partition	Yes	₹1,200–1,400/plate catering only	Outside vendors typical	B — huge footfall, not youth-specific	B
Grandé Imperial Banquets	Andheri W	Banquet hall	8,000 sqft	Likely	Not listed	In-house	B — standard banquet crowd	B
Bonobo	Bandra W	Bar, indoor+outdoor	2,800 sqft split	Indoor portion only	Not listed	In-house bar	A — RA.co-listed nightlife spot	B
J.K. Banquets	Prabhadevi/Dadar	AC banquet hall	7,000 sqft (500–1000 pax)	Yes	Not listed	In-house	C — generic banquet crowd	B
The Palace Halls	Worli	Banquet ballroom	15,876 sqft + 3,528 sqft patio	Yes	Not listed	In-house	B — premium, not nightlife-branded	B

Venue	Area	Type	Size	AC?	Rate	F&B	Crowd-pull	Tier
Quest Coworks	Andheri	Coworking / film-shoot floor	Flexible, day-hire	Yes	Not listed	Outside catering allowed	C — zero built-in audience	B
Verbena BrewPub & SkyGarden	Lower Parel	Rooftop brewpub	10,000 sqft	No — open rooftop	Not listed	In-house	A crowd, wrong format	B
Renaissance Mumbai Convention Centre	Powai	Hotel convention	Large, flexible	Yes	Premium expected	In-house only, licensed bar	C — corporate crowd	C
Soho House Mumbai	Worli	Members' club	Not listed	Yes	Members-only	High-end in-house	Access-restricted — unlikely to host a public loud event	C

Call these 5 first: Mehboob Studios (best open-floor + gig audience) → Hard Rock Cafe Andheri (built-in nightlife crowd) → Doolally Taproom Andheri (proven games+beer crowd) → Todi Mill Social (Kamala Mills bar-hop density) → NESCO (ask specifically for a sub-3,000 sqft partitioned hall). **Ask every one:** exact clear sq ft with furniture out · AC confirmed for the specific hall, not just the building · floor material and barricade/ramp tolerance · noise tolerance for DJ + RC motors · F&B — in-house only vs outside catering/food-truck allowed vs F&B minimum · day-rate vs min-spend vs door-split · capacity for 100–300 pax.

2. Scenario B — Indoor AC sports turf

Scenario B — Indoor AC sports turf

TORQWARS

Badminton/cricket/football turf already down · example 14 x 11 m box · walls/net do most of the containing

Standard 2v2/3v3 → 4–6 drivers live · Big Party 4v4/6v6 → 8–12 (Rulebook §4/§5).

Walls/net already contain 3 sides — no barricade build there, only a soft line on the open side.



What we'd need: almost nothing structural — the turf, walls and (usually) a net are already there.

- The pitch itself: **6.5 × 10 m ≈ 700 sq ft**, per [TorqBall — Rulebook §3](#)
- The ramp kit **scattered across an obstacle zone** beside the pitch (not a straight lane) — chicanes and jumps placed informally, same modular design as Scenario A
- A driver stand, sized to the Big Party peak (8–12 concurrent drivers) per Rulebook §4/§5
- A soft noodle line on the one open side only — the walls/net already contain the other three
- Goals with LED
- A small DJ/dance corner
- Pit + charging table
- Watcher seating (~30–40 pax standing rail)
- A scoreboard or projection

This is the build reused from the original turf short-run plan — same modular ramp design, same rented-fleet rule, no barricade fabrication.

The honest gap from the last research pass (still true): no Mumbai indoor turf could be web-confirmed as genuinely air-conditioned — "indoor" usually means a roofed shed or mall floor with fans, not a chilled hall. Every AC claim below needs a phone call.

New this pass — event-hosting + food:

Venue	Area	Event-booking allowed?	F&B / outside catering	Bar?	Tier
Kick Powai / A Team Sports , Supreme Business Park	Powai	Yes, explicit — markets corporate events + private parties, custom quote	In-house café; outside-catering stance unverified	Unverified	A
Tiger Play, Citi Mall (rooftop)	Andheri W	Yes — bookable "for your next match or event"	Real working kitchen (not just vending) — outside catering likely in-house-only	Unverified	A
Goregaon Sports Club	Malad W	Yes, explicit — banquet booking, 50% deposit, halls to 150 pax, centralised AC (club, not a pure turf — has separate indoor badminton/squash/TT)	In-house restaurants (Water Front Café, Bleu Restobar), from ₹1,000/plate	Restobar on premise — unverified for events	B (fallback/hybrid)
Xylo Sports (Gravity Ball Park)	Mahakali Caves Rd, Andheri E	Unverified	Unverified — note a separate "Xylo Banquet & Lawn/Hall" listing at same locality, link unconfirmed	Unverified	B
Smaaash	Lower Parel	Yes — AC hall to 100 pax, 10-day advance	In-house only, outside catering not allowed ; buffet from ₹2,000/plate	Unverified	B (branded activation, not a turf)
Trickshot (High Street Mall Thane / Mindspace Airoli)	Thane / Navi Mumbai	Unverified — sport-slot pages only	Unverified	Unverified	C
Inbox Woods, Futsal Association Marol, Turf House Mira Road, Wings Sports Bandra, Turf Station Juhu, Padel 360 Privé Lower Parel	Various	Unverified	Unverified	Unverified	C

Catering options for a 50–150 pax daytime event (₹250–500/head budget band): **CaterNinja** (Mumbai food-truck marketplace, dedicated "food trucks for party" category) · **PartyOne** (Mumbai food-truck aggregator) · **Jaffer Bhai's Catering** (published corporate price list, ₹200–1,200/plate depending on menu) · mocktail live-counters (Bottoms Up Mocktails and similar, 20+ flavours, typically capped ~100 serves).

Call these 3 first: Kick Powai (only venue that explicitly advertises private-party packages) → Tiger Play Citi Mall (bookable for events, real kitchen) → Goregaon Sports Club as a hybrid fallback (confirmed event process, but verify the turf/court can actually be booked alongside the banquet hall for our layout).

3. Scenario C — Outdoor turf



What we'd need: the ground's own boundary does most of the containing — hard barricades are mostly skipped.

- The pitch itself: **6.5 × 10 m ≈ 700 sq ft**, per [TorqBall — Rulebook](#) §3
- A rented **inflatable air-wall** on the one open edge instead of a hard barricade
- A rented **waterproof party tent** over the driver stand, DJ booth, dance floor and seating — the only genuinely fixed weatherproofing spend
- A smaller shade sail over the ramp/chicane obstacle zone, which stays **scattered, not a straight lane**
- A driver stand, sized to the Big Party peak (8–12 concurrent drivers) per Rulebook §4/§5
- Portable AC/cooler units — optional, priced separately, only if heat is a real concern for the date and time chosen

Venue	Area	Roofed/netted or open?	Rate signal	Private event booking?	Tier
UMRB Turf, Azad Nagar (Andheri Sports Complex)	Andheri	Netted, floodlit	Not listed	Unverified	B
Urban Sports Park – Chembur	Chembur	Open-air, seating	Not listed	Listed for "sports facilities for hire" incl. events	B
Sector 30 turf, Vashi	Navi Mumbai	Netted, floodlit, cafeteria + parking	₹1,800 wkday / ₹2,800 wkend	Unverified	B

Venue	Area	Roofed/netted or open?	Rate signal	Private event booking?	Tier
TMT – Sportsclub, Ghodbunder Rd	Thane	Open-air, 2 turfs, parking	Not listed	Unverified	B
Passion United Astro Fields	Not specified	Open-air	₹1,200 wkday / ₹1,500 wkend	Unverified — direct contact Rachna 9820087029	B
Dribble (Wadala), Footbrawl (Santacruz W), Kick Off (Oshiwara), Totally Turf (Chembur), Futsal (Mulund), Indian Football School (Andheri)	Various	Mostly rooftop/netted	₹1,200–2,500/hr	Unverified	B
Turf Square, Navi Mumbai Merchant Gymkhana	Vashi	Open-air, club grounds	Not listed	Club grounds — often open to private bookings	B

Inflatable air-wall / decor vendors: High Flyers Balloons & Inflatables (Mumbai manufacturer — inflatable arch gates, weather-resistant nylon, positions itself for sports/festival events; no price listed) · local balloon/inflatable-arch vendors via Justdial directories. **Gap:** no Mumbai-specific vendor for inflatable *air-wall fencing* or inflatable lounge furniture surfaced in this pass — call High Flyers directly and ask if they can source it, since only balloon-arch and bouncy-castle listings came up.

Portable cooling: general portable AC rental ~₹2,000/day + transport (IndiaMart-listed vendors) · mist fans / air coolers from Sulekha/MoreRentals/KirayNow-style rental sites — commonly used for outdoor weddings, no firm day-rate found, described as budget-friendly.

Call these 5 first: UMRB Turf Azad Nagar (netted, floodlit, sports-complex scale) → Urban Sports Park Chembur (already listed for hire, has seating) → Sector 30 Vashi (netted, floodlit, cafeteria+parking — largest amenity set found) → TMT Sportsclub Thane (two turfs, ample parking, room for inflatable decor) → Passion United (has a direct human contact, useful for a fast DJ/party yes-or-no).

Caveat that applies to all of Scenario C: none of these sources confirm a "DJ + RC-car party" booking directly — one listing (a school ground) flags royalty charges apply for DJ/livestream setups, implying it's conditional rather than default elsewhere too. Confirm noise/DJ terms on the same call as the sq ft question.

4. DIY vs vendor — keep it capex-light


The instruction driving this plan: **reduce vendor dependence wherever we can build it ourselves.** Split below.

Item	Build it ourselves (DIY)	Use a vendor	Why
Ramp kit (up-ramp / deck / roller modules)	Yes — plywood + EVA foam + chevron tape, one weekend, ~₹6,000–9,000/kit	—	Same design in all 3 scenarios, fully reusable event to event, no reason to outsource a plywood-and-foam build
Goals + LED	Yes , build (frame + LED strip on a power bank) — or buy a basic Decathlon 5-a-side goal pair (~₹2,000–4,000/pair) and add our own LED	Only the LED strip/driver if we don't want to solder	Decathlon goals are a legitimate cheap alternative to building from scratch — compare both before committing
Barricades (Scenario A only)	Yes , modular panels (same construction logic as the boarded-pitch panels in TorqBall — Ball & Boards Test) — the one big carpentry job in Scenario A	—	A rented barricade system runs ~₹150–300/linear metre/day and adds up fast over a full 4-side perimeter; building once and reusing is cheaper past event #1
Driver stand + backdrop	Yes — stage decks or pallets + ply, same design across all 3 scenarios	Stage-deck rental is a cheap fallback if timeline is tight (~₹800–1,600/day)	Either way it's the smallest line item
Branding print (backdrop, banners, stand skirt, wristbands)	—	Vendor — flex/fabric printing, wristbands	The one place print quality actually matters on camera; DIY printing looks DIY

Item	Build it ourselves (DIY)	Use a vendor	Why
Inflatable air-wall (Scenario C only)	—	Vendor — rented per event	Not a buildable item; renting is the only realistic route
Party tent (Scenario C only)	—	Vendor — rented per event	Same — weatherproofing needs a real waterproof structure
Portable AC/cooler (Scenario C, optional)	—	Vendor — rented per event	Not worth owning for one event
DJ + sound system	—	Vendor or a friend with gear	Standard party-hire item, not worth building
Food/drink	—	Vendor — food truck or light catering (\$2 list)	Never DIY catering for a public event
PA / scoreboard / projection	Yes if a laptop + projector + speaker already exist	Vendor rental if not	Cheapest possible AV is fine for a short run

Net effect: the only hard vendor dependencies across all three scenarios are branding print, DJ/sound, and food — everything physically built (ramps, goals, barricades, stand) is DIY and reusable at every event after this one. Scenario C adds two more unavoidable rentals (tent, inflatable wall) because weatherproofing and soft fencing aren't buildable in a week.

5. Build timeline — location in 5 days, build in 7

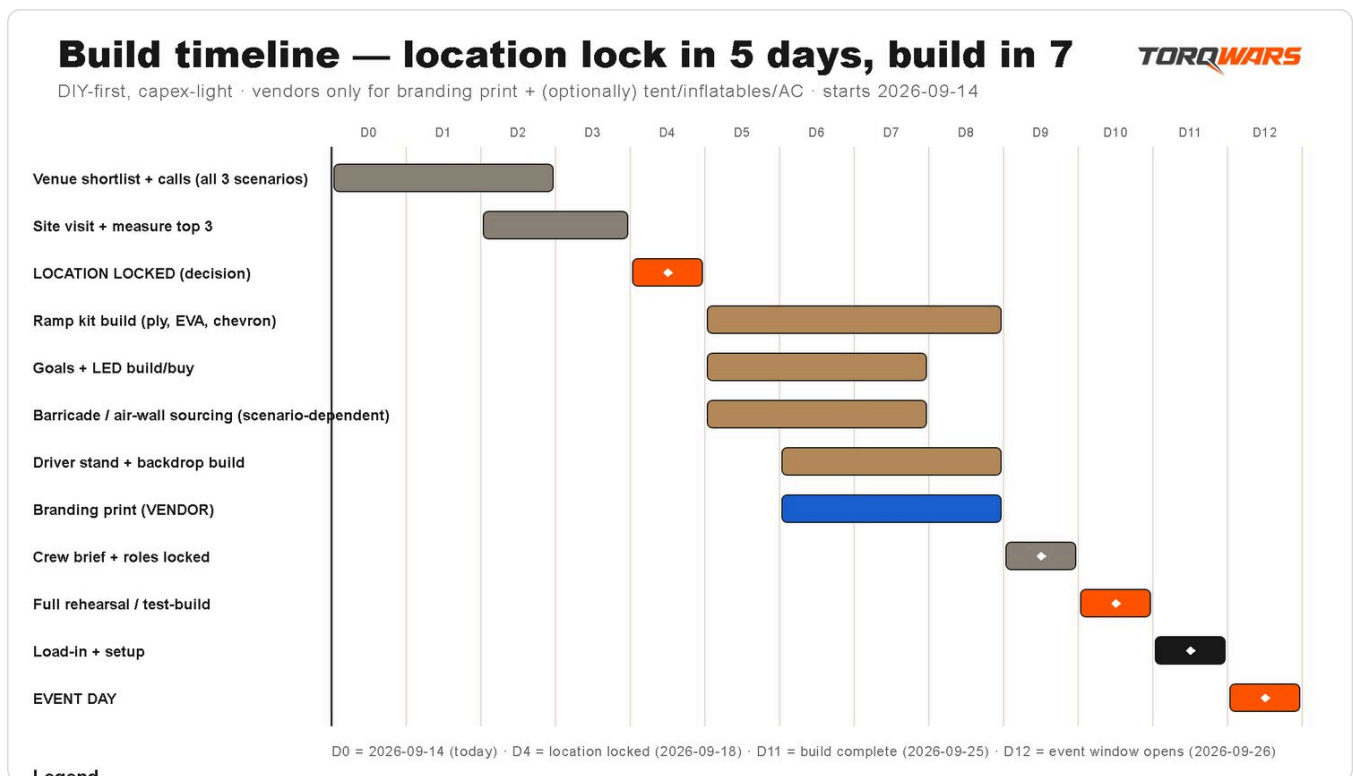

Day	Date	Milestone
D0–D3	2026-09-14 → 09-17	Venue shortlist + calls across all 3 scenarios (§1–§3 call lists)
D2–D3	2026-09-16 → 09-17	Site visit + measure the top 3 candidates (overlaps the tail of the call round)
D4	2026-09-18	LOCATION LOCKED — the one decision that gates everything after it
D5–D8	2026-09-19 → 09-22	Ramp kit build (ply, EVA, chevron) — 4 days, the longest DIY job

Day	Date	Milestone
D5–D7	2026–09–19 → 09–21	Goals + LED build/buy, in parallel
D5–D7	2026–09–19 → 09–21	Barricade sourcing/build (Scenario A) or air-wall + tent booking (Scenario C) — scenario-dependent, in parallel
D6–D8	2026–09–20 → 09–22	Driver stand + backdrop build
D6–D8	2026–09–20 → 09–22	Branding print ordered (vendor , the one item with real lead time)
D9	2026–09–23	Crew brief + roles locked
D10	2026–09–24	Full rehearsal / test-build — assemble everything once before the real day
D11	2026–09–25	Load-in + setup at the venue
D12	2026–09–26	EVENT DAY

Why location comes first: every build decision downstream — barricades or not, tent or not, pitch orientation, ramp-lane length — depends on which scenario wins. Nothing in §4's build list should be bought before D4.

Compressing the timeline: if a venue confirms before D4, everything after it can shift left by the same number of days — the 7-day build block is a ceiling, not a floor, once the ramp kit and goals are largely mode-independent.
