

# TorqBall — Venue Scenarios & Build Plan v1

Three venue types for the TorqBall short-run event, compared side by side, with a floor plan for each and one build timeline. Desk research, Mumbai, Sept 2026 — nothing below has been phone-confirmed or booked. Game rules stay as in [TorqBall — Rulebook](#); the fleet rule stays as in [Car Fleet, Scale & Protection](#). Starts from today, **2026-09-14**; location locked by **2026-09-18** (5 days), build complete by **2026-09-25** (7 days), event window opens **2026-09-26**.

## 0. The three scenarios at a glance


|                              | A — Indoor AC raw hall                                             | B — Indoor AC sports turf                                   | C — Outdoor turf                                                                   |
|------------------------------|--------------------------------------------------------------------|-------------------------------------------------------------|------------------------------------------------------------------------------------|
| What it is                   | Empty AC hall / mall unit / banquet floor — nothing exists on site | Badminton/cricket/football turf, indoor, AC                 | Open-air cricket/football ground, no AC                                            |
| Ground                       | We lay our own turf/gym mat                                        | Already down                                                | Already down                                                                       |
| Barricades                   | <b>Full build, all 4 sides</b> — no walls to use                   | Mostly skipped — walls/net contain 3 sides, one soft line   | Mostly skipped — ground boundary + rented inflatable air-wall                      |
| Goals                        | Build or buy (Decathlon) + LED, from scratch                       | Build or buy + LED                                          | Build or buy + LED                                                                 |
| Ramps                        | Same modular kit, scattered directly on the pitch, in all 3        | Same modular kit, scattered directly on the pitch, in all 3 | Same modular kit, scattered directly on the pitch, in all 3                        |
| Weatherproofing              | N/A — already indoors                                              | N/A — already indoors                                       | <b>Needed</b> — tent over stand/DJ/seating                                         |
| Cooling                      | Already AC                                                         | Already AC                                                  | Portable AC/cooler units, optional                                                 |
| Capex (build-only, ex-venue) | <b>Highest</b> — everything fabricated                             | <b>Lowest</b> — reuses venue structure                      | <b>Middle</b> — tent + inflatables replace hard barricades                         |
| Control                      | Full — layout, branding, sightlines on every surface               | Partial — pitch orientation fixed by the turf shape         | Full on the ground, weather is the wildcard                                        |
| Best for                     | A hero, branding-heavy shoot if budget allows                      | The fastest, cheapest way to get a live match on camera     | If a genuinely large, cheap ground is available and the date has good weather odds |

## 1. Scenario A — Indoor AC raw hall

## Scenario A — Indoor AC raw hall

**TORQWARS**

Full-build rig · example 20 x 15 m (~3,230 sq ft) empty AC hall/mall unit/banquet floor · we build everything

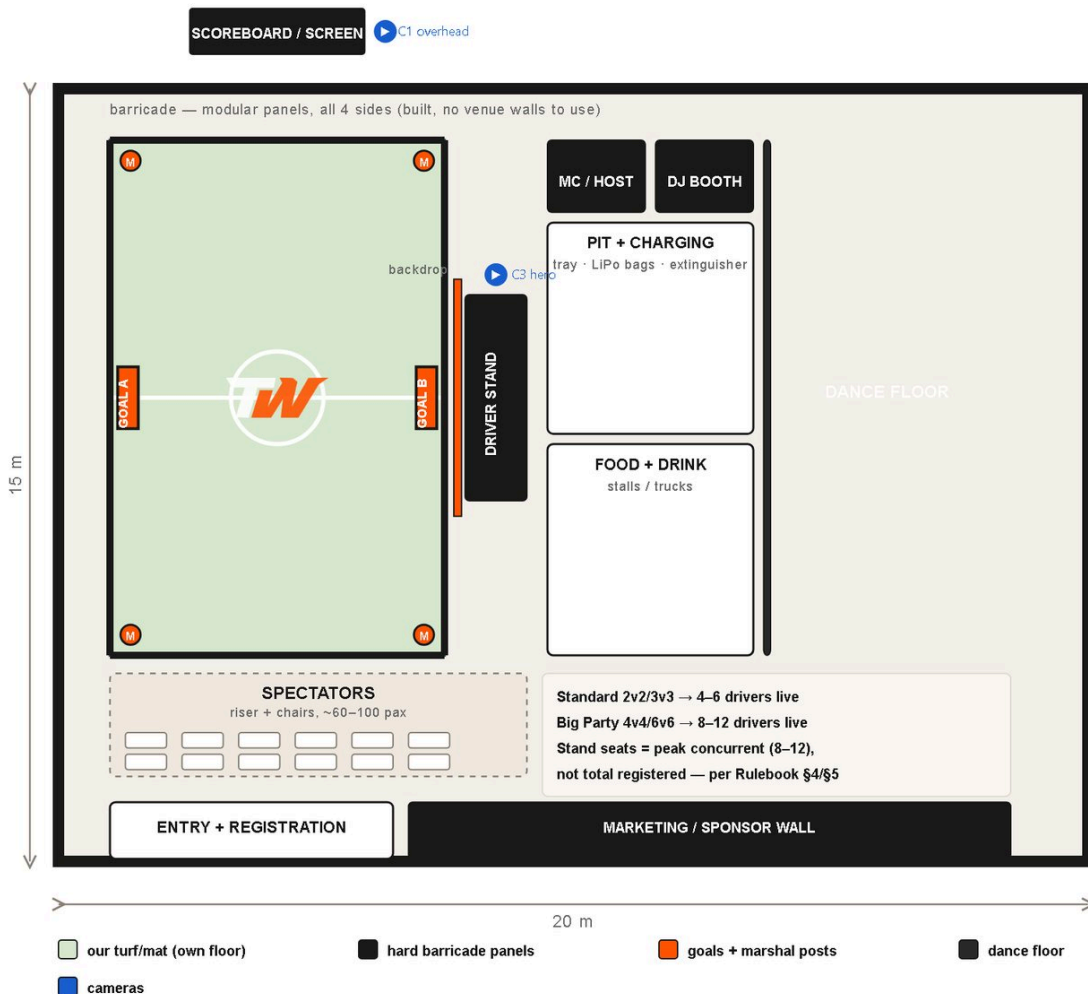

Everything here is built by us — highest capex + labour of the 3 scenarios, but full control of layout, sightlines and branding on every surface.

### What we'd need to build, top to bottom:

- Modular barricade panels on all four sides — nothing here is contained by the venue itself
- Our own turf or gym-mat flooring for the pitch — **6.5 × 10 m ≈ 700 sq ft**, the real dimension from [TorqBall — Rulebook](#) §3, not a guess
- Two goals with LED, built or Decathlon-bought
- The ramp kit **scattered directly on the pitch itself**, not a fixed lane — chicanes and jumps placed informally so cars find them while free-driving, the way the field itself makes the game fun
- A driver stand facing the pitch, backdrop behind it for the hero shot — **seats sized to the Big Party peak (8–12 concurrent drivers), not to total attendance**, per Rulebook §4/§5
- An MC stand
- A DJ booth

- A dance floor big enough for 20–30 people
- Spectator seating (riser + chairs, ~60–100 pax)
- Pit + charging table
- Food/drink stalls
- Entry/registration desk
- A marketing/sponsor wall
- A scoreboard or screen
- An overhead camera rig

**Why it costs more:** every one of those is a fabrication or a rental, because the room starts empty. This is the only scenario where hard barricades run the full perimeter — budget them like the boarded-arena spend in [TorqBall — What The Event Needs](#) §2, not the light noodle-line from a turf scenario.

**Where it wins:** total control. The pitch, stand, DJ booth and dance floor can all be positioned for the best camera angles and the branding covers every surface, since nothing pre-exists to work around.

### Venue shortlist (web desk research — not phone-confirmed)

| Venue                                     | Area             | Type                        | Size                                             | AC?                                         | Rate                             | F&B                                  | Crowd-pull                                    | Tier |
|-------------------------------------------|------------------|-----------------------------|--------------------------------------------------|---------------------------------------------|----------------------------------|--------------------------------------|-----------------------------------------------|------|
| <b>Mehboob Studios</b>                    | Bandra W         | Film studio → concert venue | Large soundstage, sq ft not listed               | Unconfirmed (studio — may need portable AC) | Not listed                       | Likely outside catering allowed      | <b>A</b> — active concert venue               | A    |
| <b>Hard Rock Cafe</b>                     | Andheri W        | Restaurant/music venue      | Banquet 375–600 pax                              | Yes                                         | Not listed                       | In-house kitchen+bar, likely F&B min | <b>A</b> — global nightlife brand             | A    |
| <b>Doolally Taproom</b>                   | Andheri W        | Brewery/taproom             | ~250-guest hall claim                            | Yes                                         | Not listed                       | In-house brewery                     | <b>A</b> — existing games+beer crowd          | A    |
| <b>Todi Mill Social</b><br>(Kamala Mills) | Lower Parel      | Lounge/bar                  | 300 seated / 450 floating                        | Yes                                         | Not listed                       | In-house bar/kitchen                 | <b>A</b> — densest bar-hop district in Mumbai | A    |
| NESCO / Bombay Exhibition Centre          | Goregaon E       | Exhibition halls            | Smallest hall ~22,700 sqft — ask for a partition | Yes                                         | ₹1,200–1,400/plate catering only | Outside vendors typical              | B — huge footfall, not youth-specific         | B    |
| Grandé Imperial Banquets                  | Andheri W        | Banquet hall                | 8,000 sqft                                       | Likely                                      | Not listed                       | In-house                             | B — standard banquet crowd                    | B    |
| Bonobo                                    | Bandra W         | Bar, indoor+outdoor         | 2,800 sqft split                                 | Indoor portion only                         | Not listed                       | In-house bar                         | A — RA.co-listed nightlife spot               | B    |
| J.K. Banquets                             | Prabhadevi/Dadar | AC banquet hall             | 7,000 sqft (500–1000 pax)                        | Yes                                         | Not listed                       | In-house                             | C — generic banquet crowd                     | B    |
| The Palace Halls                          | Worli            | Banquet ballroom            | 15,876 sqft + 3,528 sqft patio                   | Yes                                         | Not listed                       | In-house                             | B — premium, not nightlife-branded            | B    |

| Venue                                | Area        | Type                         | Size               | AC?               | Rate             | F&B                         | Crowd-pull                                               | Tier |
|--------------------------------------|-------------|------------------------------|--------------------|-------------------|------------------|-----------------------------|----------------------------------------------------------|------|
| Quest Coworks                        | Andheri     | Coworking / film-shoot floor | Flexible, day-hire | Yes               | Not listed       | Outside catering allowed    | C — zero built-in audience                               | B    |
| Verbena BrewPub & SkyGarden          | Lower Parel | Rooftop brewpub              | 10,000 sqft        | No — open rooftop | Not listed       | In-house                    | A crowd, wrong format                                    | B    |
| Renaissance Mumbai Convention Centre | Powai       | Hotel convention             | Large, flexible    | Yes               | Premium expected | In-house only, licensed bar | C — corporate crowd                                      | C    |
| Soho House Mumbai                    | Worli       | Members' club                | Not listed         | Yes               | Members-only     | High-end in-house           | Access-restricted — unlikely to host a public loud event | C    |

**Call these 5 first:** Mehboob Studios (best open-floor + gig audience) → Hard Rock Cafe Andheri (built-in nightlife crowd) → Doolally Taproom Andheri (proven games+beer crowd) → Todi Mill Social (Kamala Mills bar-hop density) → NESCO (ask specifically for a sub-3,000 sqft partitioned hall). **Ask every one:** exact clear sq ft with furniture out · AC confirmed for the specific hall, not just the building · floor material and barricade/ramp tolerance · noise tolerance for DJ + RC motors · F&B — in-house only vs outside catering/food-truck allowed vs F&B minimum · day-rate vs min-spend vs door-split · capacity for 100–300 pax.

## 2. Scenario B — Indoor AC sports turf

### Scenario B — Indoor AC sports turf

TORQWARS

Badminton/cricket/football turf already down · example 14 x 11 m box · walls/net do most of the containing

Standard 2v2/3v3 → 4–6 drivers live · Big Party 4v4/6v6 → 8–12 (Rulebook §4/§5).

Walls/net already contain 3 sides — no barricade build there, only a soft line on the open side.



**What we'd need:** almost nothing structural — the turf, walls and (usually) a net are already there.

- The pitch itself: **6.5 × 10 m ≈ 700 sq ft**, per [TorqBall — Rulebook §3](#)
- The ramp kit **scattered directly on the pitch** (not a straight lane) — chicanes and jumps placed informally, same modular design as Scenario A
- A driver stand, sized to the Big Party peak (8–12 concurrent drivers) per Rulebook §4/§5
- A soft noodle line on the one open side only — the walls/net already contain the other three
- Goals with LED
- A small DJ/dance corner
- Pit + charging table
- Watcher seating (~30–40 pax standing rail)
- A scoreboard or projection

This is the build reused from the original turf short-run plan — same modular ramp design, same rented-fleet rule, no barricade fabrication.

**The honest gap from the last research pass (still true):** no Mumbai indoor turf could be web-confirmed as genuinely air-conditioned — "indoor" usually means a roofed shed or mall floor with fans, not a chilled hall. Every AC claim below needs a phone call.

**New this pass — event-hosting + food:**

| Venue                                                                                                                            | Area                         | Event-booking allowed?                                                                                                                           | F&B / outside catering                                                                             | Bar?                                        | Tier                               |
|----------------------------------------------------------------------------------------------------------------------------------|------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------|---------------------------------------------|------------------------------------|
| <b>Kick Powai / A Team Sports</b> , Supreme Business Park                                                                        | Powai                        | <b>Yes, explicit</b> — markets corporate events + private parties, custom quote                                                                  | In-house café; outside-catering stance unverified                                                  | Unverified                                  | <b>A</b>                           |
| <b>Tiger Play, Citi Mall</b> (rooftop)                                                                                           | Andheri W                    | <b>Yes</b> — bookable "for your next match or event"                                                                                             | Real working kitchen (not just vending) — outside catering likely in-house-only                    | Unverified                                  | <b>A</b>                           |
| Goregaon Sports Club                                                                                                             | Malad W                      | Yes, explicit — banquet booking, 50% deposit, halls to 150 pax, centralised AC (club, not a pure turf — has separate indoor badminton/squash/TT) | In-house restaurants (Water Front Café, Bleu Restobar), from ₹1,000/plate                          | Restobar on premise — unverified for events | B (fallback/hybrid)                |
| Xylo Sports (Gravity Ball Park)                                                                                                  | Mahakali Caves Rd, Andheri E | Unverified                                                                                                                                       | Unverified — note a separate "Xylo Banquet & Lawn/Hall" listing at same locality, link unconfirmed | Unverified                                  | B                                  |
| Smaaash                                                                                                                          | Lower Parel                  | Yes — AC hall to 100 pax, 10-day advance                                                                                                         | <b>In-house only, outside catering not allowed</b> ; buffet from ₹2,000/plate                      | Unverified                                  | B (branded activation, not a turf) |
| Trickshot (High Street Mall Thane / Mindspace Airoli)                                                                            | Thane / Navi Mumbai          | Unverified — sport-slot pages only                                                                                                               | Unverified                                                                                         | Unverified                                  | C                                  |
| Inbox Woods, Futsal Association Marol, Turf House Mira Road, Wings Sports Bandra, Turf Station Juhu, Padel 360 Privé Lower Parel | Various                      | Unverified                                                                                                                                       | Unverified                                                                                         | Unverified                                  | C                                  |

**Catering options for a 50–150 pax daytime event** (₹250–500/head budget band): **CaterNinja** (Mumbai food-truck marketplace, dedicated "food trucks for party" category) · **PartyOne** (Mumbai food-truck aggregator) · **Jaffer Bhai's Catering** (published corporate price list, ₹200–1,200/plate depending on menu) · mocktail live-counters (Bottoms Up Mocktails and similar, 20+ flavours, typically capped ~100 serves).

**Call these 3 first:** Kick Powai (only venue that explicitly advertises private-party packages) → Tiger Play Citi Mall (bookable for events, real kitchen) → Goregaon Sports Club as a hybrid fallback (confirmed event process, but verify the turf/court can actually be booked alongside the banquet hall for our layout).

### 3. Scenario C — Outdoor turf



**What we'd need:** the ground's own boundary does most of the containing — hard barricades are mostly skipped.

- The pitch itself: **6.5 × 10 m ≈ 700 sq ft**, per [TorqBall — Rulebook](#) \$3
- A rented **inflatable air-wall** on the one open edge instead of a hard barricade
- A rented **waterproof party tent** over the driver stand, DJ booth, dance floor and seating — the only genuinely fixed weatherproofing spend
- The ramp kit **scattered directly on the pitch** (not a straight lane) — same modular design as Scenarios A and B
- A driver stand, sized to the Big Party peak (8–12 concurrent drivers) per Rulebook \$4/\$5
- Spectator standing rail/mats (~50–80 pax) beside the tent
- Portable AC/cooler units — optional, priced separately, only if heat is a real concern for the date and time chosen

| Venue                                          | Area    | Roofed/netted or open? | Rate signal | Private event booking?                               | Tier |
|------------------------------------------------|---------|------------------------|-------------|------------------------------------------------------|------|
| UMRB Turf, Azad Nagar (Andheri Sports Complex) | Andheri | Netted, floodlit       | Not listed  | Unverified                                           | B    |
| Urban Sports Park – Chembur                    | Chembur | Open-air, seating      | Not listed  | Listed for "sports facilities for hire" incl. events | B    |

| Venue                                                                                                                                     | Area          | Roofed/netted or open?                | Rate signal                 | Private event booking?                        | Tier |
|-------------------------------------------------------------------------------------------------------------------------------------------|---------------|---------------------------------------|-----------------------------|-----------------------------------------------|------|
| Sector 30 turf, Vashi                                                                                                                     | Navi Mumbai   | Netted, floodlit, cafeteria + parking | ₹1,800 wkday / ₹2,800 wkend | Unverified                                    | B    |
| TMT – Sportsclub, Ghodbunder Rd                                                                                                           | Thane         | Open-air, 2 turfs, parking            | Not listed                  | Unverified                                    | B    |
| Passion United Astro Fields                                                                                                               | Not specified | Open-air                              | ₹1,200 wkday / ₹1,500 wkend | Unverified — direct contact Rachna 9820087029 | B    |
| Dribble (Wadala), Footbrawl (Santacruz W), Kick Off (Oshiwara), Totally Turf (Chembur), Futsal (Mulund), Indian Football School (Andheri) | Various       | Mostly rooftop/netted                 | ₹1,200–2,500/hr             | Unverified                                    | B    |
| Turf Square, Navi Mumbai Merchant Gymkhana                                                                                                | Vashi         | Open-air, club grounds                | Not listed                  | Club grounds — often open to private bookings | B    |

**Inflatable air-wall / decor vendors: High Flyers Balloons & Inflatables** (Mumbai manufacturer — inflatable arch gates, weather-resistant nylon, positions itself for sports/festival events; no price listed) · local balloon/inflatable-arch vendors via Justdial directories. **Gap:** no Mumbai-specific vendor for inflatable *air-wall fencing* or inflatable lounge furniture surfaced in this pass — call High Flyers directly and ask if they can source it, since only balloon-arch and bouncy-castle listings came up.

**Portable cooling:** general portable AC rental ~₹2,000/day + transport (IndiaMart-listed vendors) · mist fans / air coolers from Sulekha/MoreRentals/KirayNow-style rental sites — commonly used for outdoor weddings, no firm day-rate found, described as budget-friendly.

**Call these 5 first:** UMRB Turf Azad Nagar (netted, floodlit, sports-complex scale) → Urban Sports Park Chembur (already listed for hire, has seating) → Sector 30 Vashi (netted, floodlit, cafeteria+parking — largest amenity set found) → TMT Sportsclub Thane (two turfs, ample parking, room for inflatable decor) → Passion United (has a direct human contact, useful for a fast DJ/party yes-or-no).

**Caveat that applies to all of Scenario C:** none of these sources confirm a "DJ + RC-car party" booking directly — one listing (a school ground) flags royalty charges apply for DJ/livestream setups, implying it's conditional rather than default elsewhere too. Confirm noise/DJ terms on the same call as the sq ft question.

## 4. DIY vs vendor — keep it capex-light


The instruction driving this plan: **reduce vendor dependence wherever we can build it ourselves.** Split below.

| Item                                       | Build it ourselves (DIY)                                                                                                                                                          | Use a vendor                                                                 | Why                                                                                                                                                         |
|--------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Ramp kit (up-ramp / deck / roller modules) | <b>Yes</b> — plywood + EVA foam + chevron tape, one weekend, ~₹6,000–9,000/kit                                                                                                    | —                                                                            | Same design in all 3 scenarios, fully reusable event to event, no reason to outsource a plywood-and-foam build                                              |
| Goals + LED                                | <b>Yes</b> , build (frame + LED strip on a power bank) — or buy a basic Decathlon 5-a-side goal pair (~₹2,000–4,000/pair) and add our own LED                                     | Only the LED strip/driver if we don't want to solder                         | Decathlon goals are a legitimate cheap alternative to building from scratch — compare both before committing                                                |
| Barricades (Scenario A only)               | <b>Yes</b> , modular panels (same construction logic as the boarded-pitch panels in <a href="#">TorqBall — Ball &amp; Boards Test</a> ) — the one big carpentry job in Scenario A | —                                                                            | A rented barricade system runs ~₹150–300/linear metre/day and adds up fast over a full 4-side perimeter; building once and reusing is cheaper past event #1 |
| Driver stand + backdrop                    | <b>Yes</b> — stage decks or pallets + ply, same design across all 3 scenarios                                                                                                     | Stage-deck rental is a cheap fallback if timeline is tight (~₹800–1,600/day) | Either way it's the smallest line item                                                                                                                      |

| Item                                                        | Build it ourselves (DIY)                                   | Use a vendor                                            | Why                                                                            |
|-------------------------------------------------------------|------------------------------------------------------------|---------------------------------------------------------|--------------------------------------------------------------------------------|
| Branding print (backdrop, banners, stand skirt, wristbands) | —                                                          | <b>Vendor</b> — flex/fabric printing, wristbands        | The one place print quality actually matters on camera; DIY printing looks DIY |
| Inflatable air-wall (Scenario C only)                       | —                                                          | <b>Vendor</b> — rented per event                        | Not a buildable item; renting is the only realistic route                      |
| Party tent (Scenario C only)                                | —                                                          | <b>Vendor</b> — rented per event                        | Same — weatherproofing needs a real waterproof structure                       |
| Portable AC/cooler (Scenario C, optional)                   | —                                                          | <b>Vendor</b> — rented per event                        | Not worth owning for one event                                                 |
| DJ + sound system                                           | —                                                          | <b>Vendor or a friend with gear</b>                     | Standard party-hire item, not worth building                                   |
| Food/drink                                                  | —                                                          | <b>Vendor</b> — food truck or light catering (\$2 list) | Never DIY catering for a public event                                          |
| PA / scoreboard / projection                                | <b>Yes</b> if a laptop + projector + speaker already exist | Vendor rental if not                                    | Cheapest possible AV is fine for a short run                                   |

**Net effect:** the only hard vendor dependencies across all three scenarios are branding print, DJ/sound, and food — everything physically built (ramps, goals, barricades, stand) is DIY and reusable at every event after this one. Scenario C adds two more unavoidable rentals (tent, inflatable wall) because weatherproofing and soft fencing aren't buildable in a week.

## 5. Build timeline — location in 5 days, build in 7

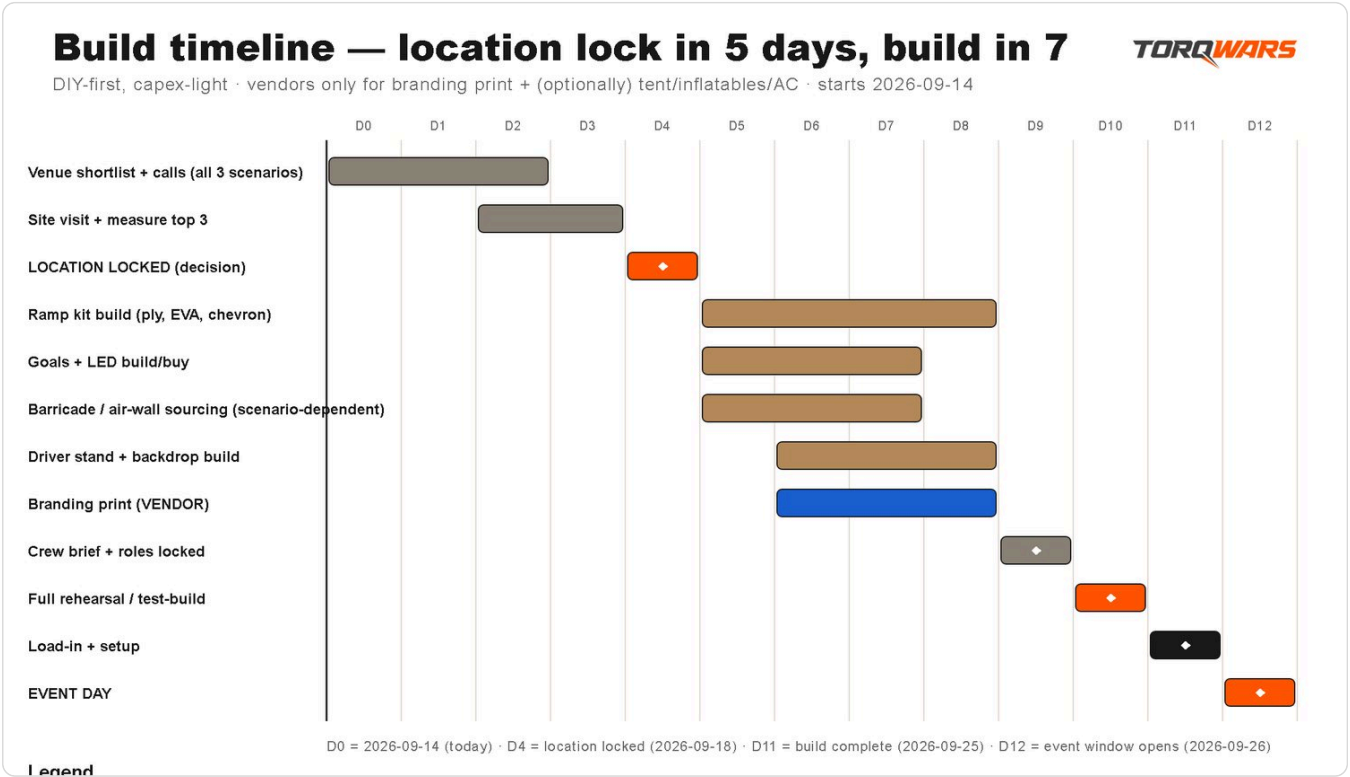

| Day   | Date               | Milestone                                                                       |
|-------|--------------------|---------------------------------------------------------------------------------|
| D0–D3 | 2026-09-14 → 09-17 | Venue shortlist + calls across all 3 scenarios (\$1–\$3 call lists)             |
| D2–D3 | 2026-09-16 → 09-17 | Site visit + measure the top 3 candidates (overlaps the tail of the call round) |

| Day        | Date               | Milestone                                                                                                       |
|------------|--------------------|-----------------------------------------------------------------------------------------------------------------|
| <b>D4</b>  | <b>2026-09-18</b>  | <b>LOCATION LOCKED</b> — the one decision that gates everything after it                                        |
| D5–D8      | 2026-09-19 → 09-22 | Ramp kit build (ply, EVA, chevron) — 4 days, the longest DIY job                                                |
| D5–D7      | 2026-09-19 → 09-21 | Goals + LED build/buy, in parallel                                                                              |
| D5–D7      | 2026-09-19 → 09-21 | Barricade sourcing/build (Scenario A) or air-wall + tent booking (Scenario C) — scenario-dependent, in parallel |
| D6–D8      | 2026-09-20 → 09-22 | Driver stand + backdrop build                                                                                   |
| D6–D8      | 2026-09-20 → 09-22 | Branding print ordered ( <b>vendor</b> , the one item with real lead time)                                      |
| D9         | 2026-09-23         | Crew brief + roles locked                                                                                       |
| <b>D10</b> | <b>2026-09-24</b>  | <b>Full rehearsal / test-build</b> — assemble everything once before the real day                               |
| D11        | 2026-09-25         | Load-in + setup at the venue                                                                                    |
| <b>D12</b> | <b>2026-09-26</b>  | <b>EVENT DAY</b>                                                                                                |

**Why location comes first:** every build decision downstream — barricades or not, tent or not, pitch orientation, ramp-lane length — depends on which scenario wins. Nothing in §4's build list should be bought before D4.

**Compressing the timeline:** if a venue confirms before D4, everything after it can shift left by the same number of days — the 7-day build block is a ceiling, not a floor, once the ramp kit and goals are largely mode-independent.
