

TorqCapture — Venue Scenarios & Build Plan v1

0. The three scenarios at a glance

	A — Indoor AC raw hall	B — Indoor AC sports turf	C — Outdoor turf
What it is	Empty AC hall / mall unit / banquet floor — nothing exists on site	Futsal/badminton/cricket turf, indoor, AC	Open-air cricket/football ground, no AC
Ground	We lay our own turf for the play area	Already down	Already down
Enclosure	Full soft rail, all 4 sides — no walls to use	Mostly skipped — walls/net contain 3 sides, one open-side rail	Ground boundary + rented inflatable air-wall
Hard barricades	Never — TorqCapture has no boarded pitch or ball to rebound	Never	Never
Capture zones	3 rings (Domination) taped/lit on our own turf	Same 3 rings, taped/lit on the venue's turf	Same 3 rings, taped/lit on the ground
Scoring rig	Overhead cam on a rigged truss/pole — built from nothing	Overhead cam on the roof/net truss if one exists, else rigged	Overhead cam on a rigged pole
Weatherproofing	N/A — already indoors	N/A — already indoors	Needed — tent over the driver stands + AV/DJ
Cooling	Already AC	Already AC	Portable AC/cooler units, optional
Capex (build-only, ex-venue)	Highest — turf, rail, stands, hub all built from nothing	Lowest — reuses venue turf and walls	Middle — tent + air-wall replace the venue's own containment
Best for	Full control of layout, sightlines and branding on every surface	The fastest, cheapest way to get Domination live on camera	If a genuinely large, cheap ground is available with good weather odds


1. Scenario A — Indoor AC raw hall

Scenario A — Indoor AC raw hall



Full-build rig · example 20 x 14 m (~3,010 sq ft) empty AC hall/mall unit/banquet floor · we lay everything, incl. the soft rail

Default 2×3 = 6 drivers live · single-zone modes 2×2 = 4 (Rulebook §3) · team ticket cap ≈18–22 teams (Full Run Plan §1)

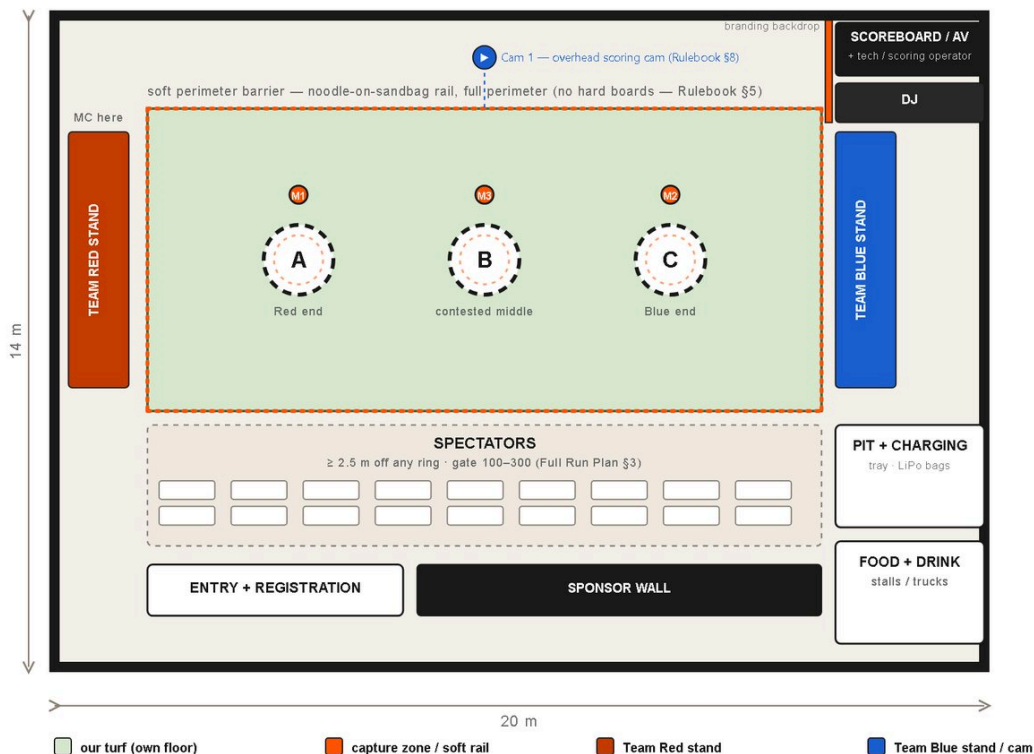

No hard barricades in any TorqCapture scenario — the soft noodle-on-sandbag rail is the only enclosure (Rulebook §5).
Highest capex here because the turf, rail, stands and hub are all built from nothing.

What we'd need to build, top to bottom:

- Our own turf for the tight-lay Domination footprint — $14.5 \times 6.5 \text{ m} \approx 1,010 \text{ sq ft}$, the fit math from [TorqCapture — What The Event Needs](#) §4, not a guess
- A soft perimeter barrier — noodle-on-sandbag rail, **full perimeter, all 4 sides** — nothing here is contained by the venue itself
- 3 capture zones (A/B/C), 1.5–2 m rings, taped ± raised foam lip ± lit LED, per [TorqCapture — Zone-Capture Tech](#)
- An overhead scoring camera rigged on a truss/pole over the play-area centre — scores every zone AND feeds the big screen
- Two mini driver stands, one per team, at the A end and the C end — sized to the default **2×3 = 6 concurrent drivers** (Rulebook §3), not to total attendance
- A scoreboard/AV table with the tech/scoring operator, plus the DJ
- Spectator standing space, entry/registration, a marketing/sponsor wall

- Pit + charging table
- Food/drink stalls

Why it costs more: the turf, the rail, both stands, the scoring rig's mount and the AV hub are all built or rigged from nothing, because the room starts empty.

Where it wins: total control. The pitch, both stands, the AV hub and the overhead cam can all be positioned for the best sightlines, and branding covers every surface since nothing pre-exists to work around.

What to look for in this venue type

- Clear sq ft with furniture out — need the tight-lay ~1,010 sq ft play footprint plus standoff and spectator space, inside the shared ~3,000 sq ft envelope (Rulebook §5)
- A genuine **ceiling/truss or rigging point over the floor centre** — the overhead scoring cam needs a mount at the height the Zone-Capture Tech bench test proves; a raw hall usually means rigging this from scratch, not finding one
- AC confirmed for the specific hall, not just the building
- Floor material and how it takes tape/rail stakes
- Power — a dedicated circuit for the charging pit, and mains for the scoring laptop + big screen
- Noise tolerance for DJ + RC motors + crowd
- F&B — in-house only vs outside catering/food-truck allowed vs F&B minimum
- Load-in door size and route for turf rolls, stands and the AV/scoring gear

2. Scenario B — Indoor AC sports turf


Scenario B — Indoor AC sports turf

TORQWARS

Futsal/badminton/cricket turf already down · example 17 x 10 m shed · walls/net contain most sides

Default 2x3 = 6 drivers live · single-zone modes drop to 2x2 = 4 (Rulebook §3).

No indoor turf could be web-confirmed as genuinely AC (same gap TorqBall found) — call and check.

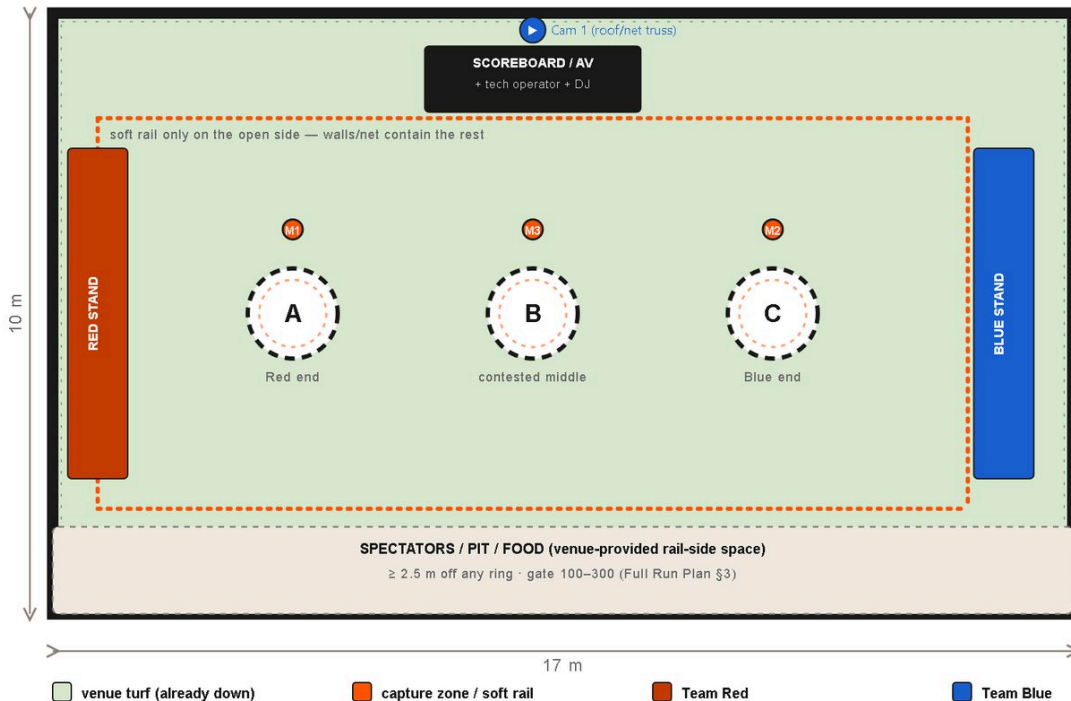

What we'd need: almost nothing structural — the turf and walls/net are already there.

- The tight-lay Domination footprint — **14.5 × 6.5 m ≈ 1,010 sq ft**, per [TorqCapture — What The Event Needs](#) §4, marked on the venue's own turf
- 3 capture zones (A/B/C), same spec as Scenario A
- A soft rail **only on the one open side** — the walls/net already contain the rest
- The overhead scoring cam rigged from the roof/net truss if one exists, else a rigged pole
- Two mini driver stands, one per team
- A scoreboard/AV table with the tech operator + DJ
- Spectator / pit / food space in the venue's own rail-side area

This is the cheapest build in the set — same modular zone kit, same rented-fleet rule, no perimeter rail to build on 3 of the 4 sides.


The honest gap carried over from TorqBall's research: no Mumbai indoor turf could be web-confirmed as genuinely air-conditioned — "indoor" often means a roofed shed with fans, not a chilled

hall. Every AC claim needs a phone call.

What to look for in this venue type

- Clear sq ft with the turf already down — confirm it can fit the 14.5 × 6.5 m tight-lay axis with standoff to spare
- AC confirmed for the actual playing shed, not just claimed in a listing
- A **roof, net-support pole or truss over the turf** the scoring cam can actually mount to, at a height the bench test can work with — the single biggest unknown a sports-turf shed introduces
- Floor material (turf pile, base) and whether tape/rail stakes are allowed
- Power for the charging pit and the scoring laptop + screen
- Noise tolerance — a shed with neighbours may cap the DJ + crowd volume
- F&B — in-house only vs outside catering vs food-truck allowed
- Load-in door and route wide enough for the driver stands and AV gear

3. Scenario C — Outdoor turf

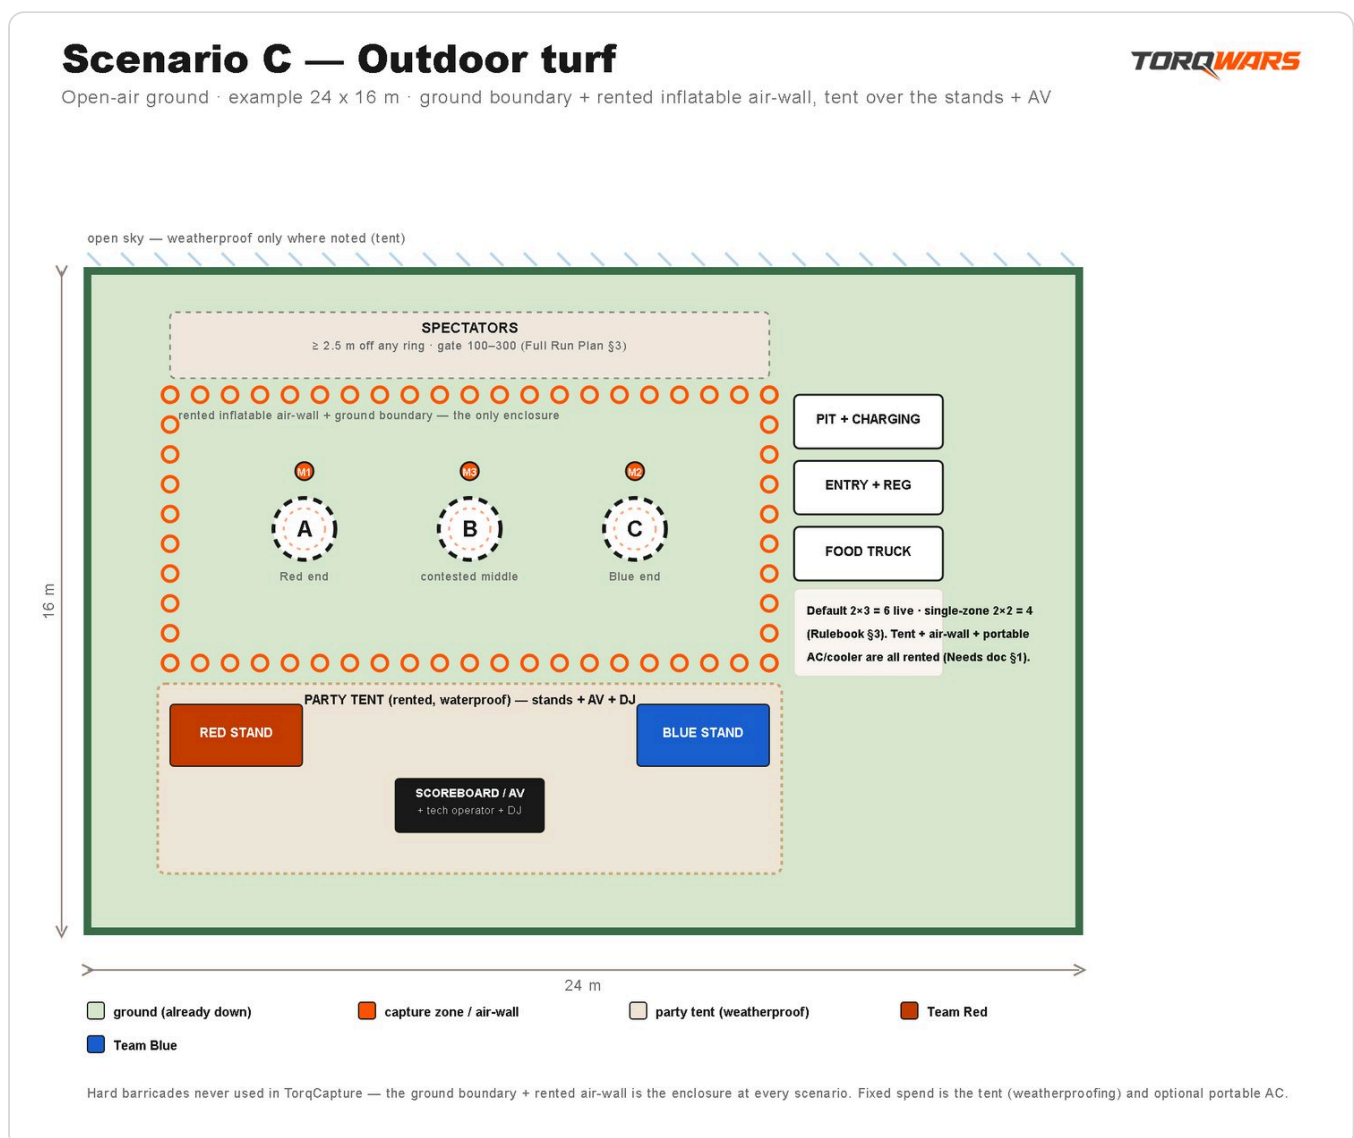

What we'd need: the ground's own boundary does most of the containing — hard barricades are never part of this game.

- The tight-lay Domination footprint — **14.5 × 6.5 m ≈ 1,010 sq ft**, per [TorqCapture — What The Event Needs](#) §4
- A rented **inflatable air-wall** around the open edges instead of a fixed barrier
- A rented **waterproof party tent** over both driver stands and the AV/DJ hub — the only genuinely fixed weatherproofing spend
- 3 capture zones (A/B/C), same spec as the other scenarios
- The overhead scoring cam rigged on a pole over the play-area centre
- Two mini driver stands, spectator standing space beside the tent
- Portable AC/cooler units — optional, priced separately, only if heat is a real concern for the date and time chosen

What to look for in this venue type

- A genuinely clear ground — enough for the 14.5 × 6.5 m footprint plus standoff, inside the shared ~3,000 sq ft envelope (Rulebook §5)
- Floor/ground surface — grass, dust, drainage after rain
- No AC by definition — check shade, time-of-day heat, and whether portable cooling is worth the spend
- Power — generator or mains for the charging pit, the scoring laptop and the big screen; the pole-mounted cam needs a reliable, weatherproofed cable run
- Noise tolerance for DJ + RC motors + crowd, and whether the ground allows amplified sound at all
- F&B — in-house vs outside catering vs food-truck allowed
- Load-in route for the tent, air-wall, stands and AV gear, and a plan if it rains on load-in day

4. DIY vs vendor — keep it capex-light


The instruction driving this plan: **reduce vendor dependence wherever we can build it ourselves**. Split below.

Item	Build it ourselves (DIY)	Use a vendor	Why
Capture zones — tape ring ± foam lip ± LED	Yes — gaffer tape is ~₹0/ring, foam lip and LED are our own build	—	Ring size and hold-timer are frozen by the Zone-Capture Tech bench test, but the physical build is ours in every scenario
Scoring camera, markers, cabling	Yes — the camera is a content buy we'd make anyway; markers are printed card/foam + velcro	—	TorqCapture — Zone-Capture Tech costs this at ~₹6,550–11,500; it's the smallest new-event delta in the whole game set
LED-driver ESP32 + 5V PSU (only with the lit-ring upgrade)	Yes — off-the-shelf parts we wire ourselves	—	Only enters cost if the lit-ring look is wanted; flat-taped rings score for ~₹0

Item	Build it ourselves (DIY)	Use a vendor	Why
Soft perimeter barrier (noodle-on-sandbag rail)	Yes — same pool-noodle-on-a-stake design in every scenario	—	Full perimeter in Scenario A, one open side in B, none needed structurally in C beyond the rented air-wall
Driver stands (Red + Blue)	Yes — pallet + ply + PVC rail, one per team	Stage-deck rental is a cheap fallback if timeline is tight	Small builds — the smallest line item in the kit
Pit + charging table	Yes , build the layout	Buy the table, charger, tray off the shelf	Standard TorqWars pit kit, reused every event
Branding print (backdrop at the AV hub)	—	Vendor — flex/fabric printing	The one place print quality matters on camera
Inflatable air-wall (Scenario C only)	—	Vendor — rented per event	Not buildable; renting is the only realistic route
Party tent (Scenario C only)	—	Vendor — rented per event	Same — weatherproofing needs a real waterproof structure
Portable AC/cooler (Scenario C, optional)	—	Vendor — rented per event	Not worth owning for one event
DJ + sound system	—	Vendor or a friend with gear	Standard party-hire item
Food/drink	—	Vendor — food truck or light catering	Never DIY catering for a public event
Scoreboard / AV	Yes — a laptop + TV/projector already exist; the same laptop runs OpenCV	Vendor rental if not owned	Cheapest possible AV is fine, and it's also the scorer

Net effect: TorqCapture fabricates almost nothing physical — no gauntlet kit, no castle stock, no boarded pitch. The only real vendor dependencies across all three scenarios are branding print, DJ/sound, food, and (Scenario C only) the tent + air-wall + optional AC. Everything else — zones, rail, stands, the scoring rig itself — is DIY and reused every event after this one.

5. Build timeline — location in 5 days, scoring rig proven in 7

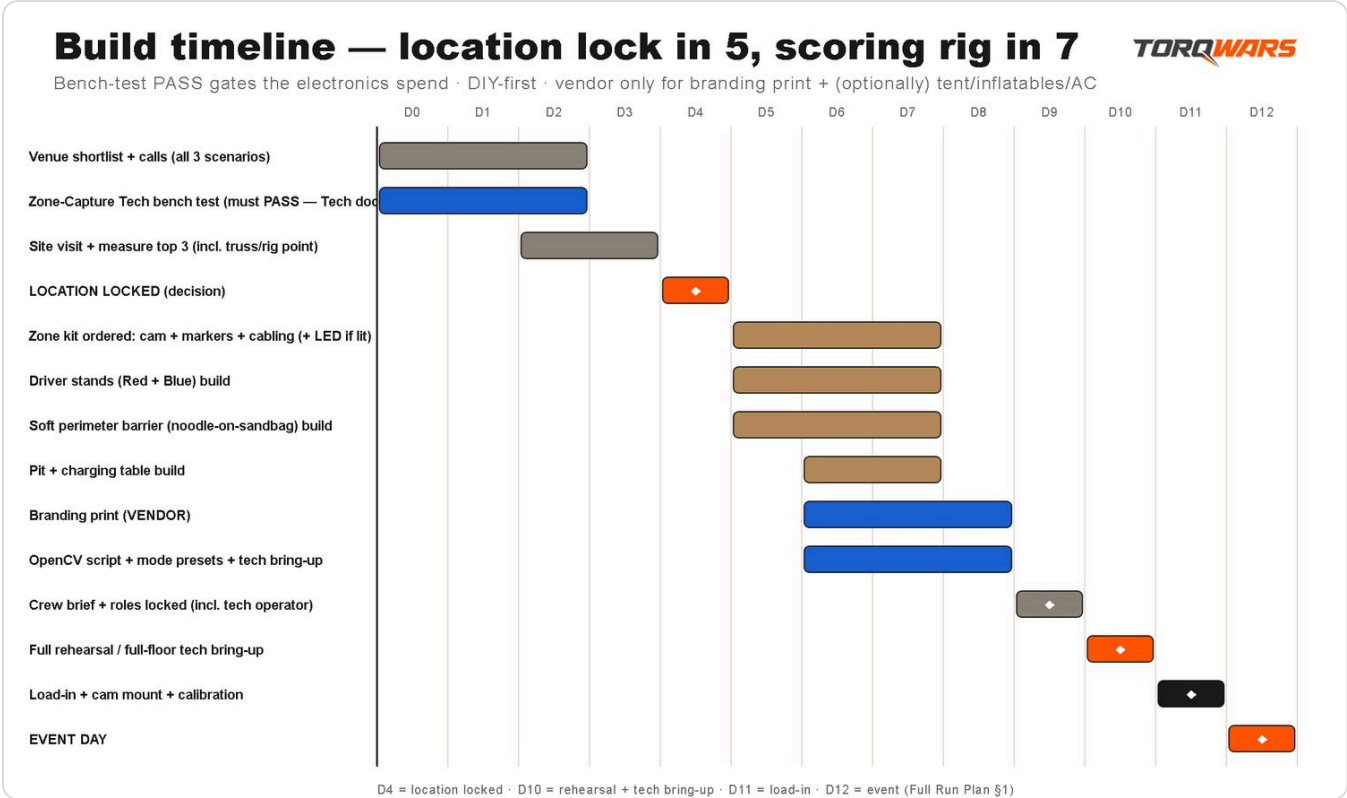

Day	Milestone
D0–D3	Venue shortlist + calls across all 3 scenarios, run in parallel with the TorqCapture — Zone-Capture Tech bench test — the electronics gate must PASS before any camera or LED spend
D2–D3	Site visit + measure the top 3 candidates, including the ceiling/truss/rig point for the overhead cam
D4	LOCATION LOCKED — the decision that gates the scenario-dependent build (rail all 4 sides vs one side vs air-wall + tent)
D5–D7	Zone kit ordered and built: camera, printed marker tops, cabling, mounts — gated on the bench test's full-span coverage trial deciding one cam vs a second stitched cam
D5–D7	Driver stands (Red + Blue) build, in parallel
D5–D7	Soft perimeter barrier build, in parallel
D6–D7	Pit + charging table build
D6–D8	Branding print ordered (vendor , the one item with real lead time)
D6–D8	OpenCV script + all 5 mode presets finished, plus a bench-scale end-to-end pipeline test
D9	Crew brief + roles locked — including the new tech/scoring operator role

Day	Milestone
D10	Full rehearsal + full-floor tech bring-up — the scoring rig must score reliably under a real multi-car pile-up, or the day runs marshal-scored
D11	Load-in + cam mount + calibration at the venue
D12	EVENT DAY

Why location comes first: the enclosure (full rail vs partial vs air-wall + tent), the turf buy, and the truss height available for the overhead cam all depend on which scenario wins. Nothing in §4's build list should be bought before D4.

Why the tech gate runs alongside, not after: the [TorqCapture — Zone-Capture Tech](#) bench test is near-zero cost and doesn't need the venue — run it in parallel with the venue calls so the tech decision (CV primary vs UHF fallback, one cam vs two) is already made by the time the D5 buy list goes out.

Compressing the timeline: if a venue confirms before D4, everything after it can shift left by the same number of days — the zone kit and stands are largely venue-independent once the scenario (and therefore the enclosure type) is known.

Pairs with: [TorqCapture — Rulebook](#) · [TorqCapture — What The Event Needs](#) · [TorqCapture — Zone-Capture Tech](#) · [TorqCapture — Full Run Plan](#) · [TorqCapture — Design Study v1](#) · [Car Fleet, Scale & Protection](#) · [Event Ops Standards \(all games\)](#).
